

Level One Compliance Report

BULK EARTHWORKS FILLING OPERATIONS Everleigh Estate Precinct 10.2

24 April 2024


Prepared By

MORRISON GEOTECHNIC

Prepared for:

Shadforth Civil

Document Reference: PTP/11755-P10.2



MORRISON
GEOTECHNIC

Gold Coast Office
Job No: PTP/11755
Ref No: P10.2
Author: Gary Taylor

24 April 2024

Shadforth Civil
99 Sandalwood Lane
Forest Glen Qld 4556

ATTENTION: CALLUM WATTS
Email: callum.watts@shadcivil.com.au

**RE: LEVEL ONE COMPLIANCE REPORT FOR BULK EARTHWORKS FILLING OPERATIONS,
EVERLEIGH ESTATE – PRECINCT 10.2, TEVIOT ROAD, GREENBANK**

1.0	INTRODUCTION	2
1.1	General.....	2
1.2	Previous Earthworks	4
1.3	The Project	4
2.0	THE BRIEF	4
2.1	Additional Requirements	4
3.0	METHODOLOGY	5
3.1	Stripped Surface Assessment.....	5
3.2	Filling Operations	6
4.0	STATEMENT OF COMPLIANCE	9
5.0	EXCLUSIONS	9
6.0	LIMITATIONS	9
	ATTACHMENTS:	10
	Appendix A – Site Plans Showing Test Locations	10
	Appendix B – Laboratory Test Results Reports.....	10

1.0 INTRODUCTION

1.1 General

This report presents results of Level One Earthworks Inspections and associated compaction compliance testing carried out on earthworks fill constructed at Everleigh Estate – Precinct 10.2, Teviot Road, Greenbank (the site).

Earthworks operations were carried out by Shadforth Civil.

Earthworks filling operations for Precinct 10.2 allotments and roads were carried out between 5 April and 27 July 2023.

The areas of fill covered by this report are presented as Figures 1, 2 and 3 below.

Figure 1 presents the extent of earthworks as shown on the Premise Earthworks Drawings MIR-1002-C200-B and MIR-1002-C201-B.

Figures 2 and 3 show the actual fill areas and conformance with the 600mm and 100mm below finished surface level as shown on the Shadforth Civil Survey Plans.

Figure 1: Extent of Fill - Premise Earthworks Drawings MIR-1002-C200-B and 201-B



Figure 2: Actual Constructed Area of Fill (600mm BFSL) – Shadforth Survey Plans


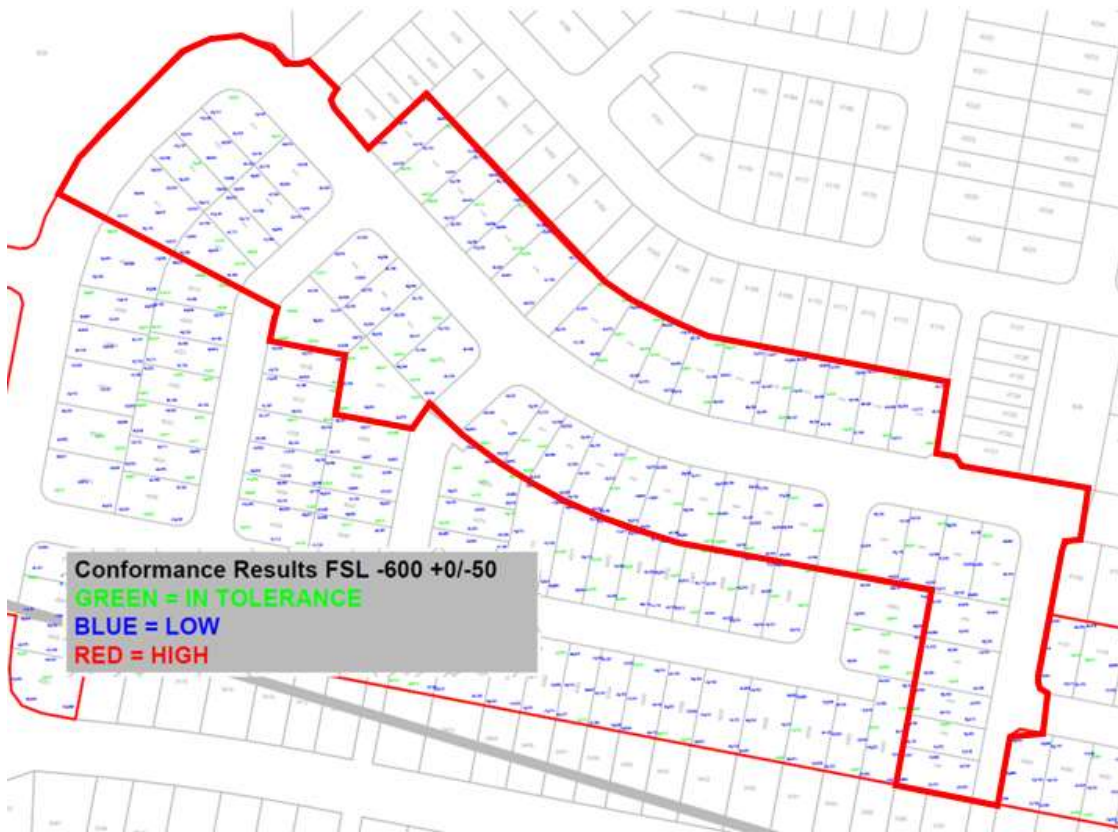


Figure 3: Actual Constructed Area of Fill (100mm BFSL) – Shadforth Survey Plans

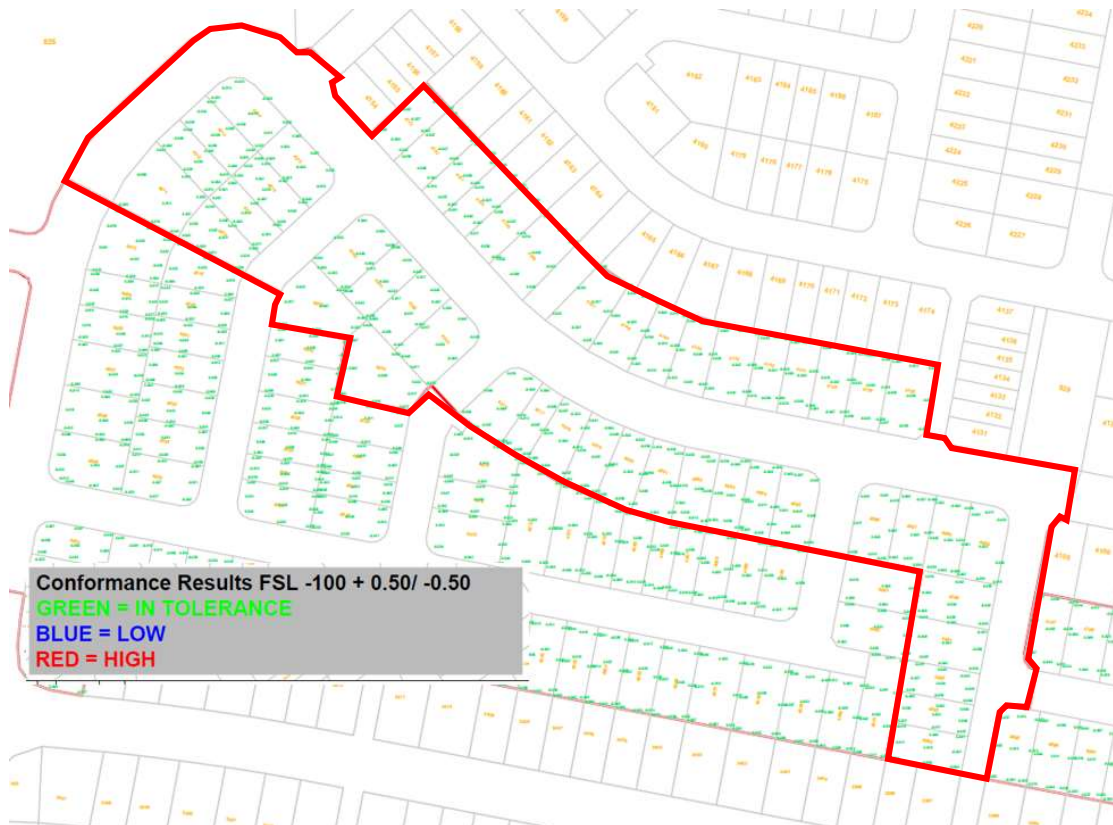

1.2 Previous Earthworks

As far as Morrison Geotechnic are aware, there were no previous earthworks at the Site.

1.3 The Project

The project includes filling operations to construct building platforms to support proposed residences, new pavements, and underground services. The Site is bounded by future precincts to the north, west, east and south.

2.0 THE BRIEF

The Brief from the Client and relevant documents were limited to:

- Level One Inspection and Testing of the placement and compaction of fill materials in general accordance with AS3798 2007 – “Guidelines on Earthworks for Commercial and Residential Developments”.
- Relative Density Control Testing in accordance with AS1289 – Testing of Soils for Engineering Purposes and at frequencies required in AS3798 Table 8.1.
- Earthworks Notes on drawings MIR-1002-C200-B and MIR-1002-C201-B.
- Recommendations in Morrison Geotechnic report “Recommended Filling Earthworks Specification” report 16520B, dated 25th June 2020.

All other design requirements such as CBR and Quality of Materials, site classification, material assessments, foundation assessments and slope / global stability appraisals were not included in the Brief and are therefore excluded from this Report.

For the actual constructed fill thickness and extremities on fill placed, a disclosure plan should be requested from the developer.

2.1 Additional Requirements

All fill at The Site was to be constructed in accordance with the Earthworks Specification as shown on Premise Drawing – MIR-0906-C200-B. The earthworks specification is presented as Figure 4 below.

Figure 4 Earthworks Specification

SPECIFICATION	DEPTH RANGE (m)				PAVEMENT SUBGRADE	TRENCH BACKFILL
	0.0 - 0.6	0.6 - 3.00	3.00 - 5.00	> 5.00		
CBR %	-	-	-	-	10	15
LAYER THICKNESS (mm)	300	300	300	300	BETWEEN SUBGRADE AND 0.3m BELOW	300
MAXIMUM PARTICLE SIZE (mm)	200	500	500	500	200	200
% PASSING 37.5mm	80% MIN	REFER NOTES AND KEY OUTCOMES	REFER NOTES AND KEY OUTCOMES	REFER NOTES AND KEY OUTCOMES	REFER NOTES AND KEY OUTCOMES	REFER NOTES AND KEY OUTCOMES
% PASSING 0.075mm	30% MIN	REFER NOTES	REFER NOTES	REFER NOTES	REFER NOTES	REFER NOTES AND AS3798
COMPACTION	95% STD	95% STD	95% STD	95% STD	100% STD	95% MOD IN ROADS AND 95% STD OUTSIDE ROADS
MOISTURE	+/- 2% OMC	+/- 2% OMC	+/- 2% OMC	+/- 2% OMC	60% - 90% OF OMC	+/- 2% OMC
<p>NOTES:</p> <ol style="list-style-type: none"> 1. OMC - OPTIMUM MOISTURE CONTENT 2. LAYER OF THICKNESS IS LIMITED TO 300mm TO ALLOW IDENTIFICATION OF LARGER PARTICLES AND ALLOW EVERY CHANCE OF BREAK DOWN IN FILLING OR REMOVAL. 3. TREATMENT OF ROCK TO SIZES ABOVE SHOULD BE CARRIED OUT IN CUT PRIOR TO LOADING TO FILL AREAS. TREATED ROCK TO BE APPROVED BY GITA PRIOR TO TRANSPORTING. 4. UPPER 0.6m, PARTICULARLY IN AREAS OF DEEP FILL, OF THE FILL PROFILE TO BE RELATIVELY IMPERMEABLE HENCE INCREASE IN FINES COMPONENT. 5. PROOF ROLL TESTING ON EACH COMPACTED LAYER USING RUBBER WHEELED PLANT SUCH AS LOADED ADT'S OR LOADED SCRAPERS. UNFAVOURABLE DEFORMATION OF THE COMPACTED SURFACE UNDER LOAD OF ADT'S OR SCRAPERS WILL REQUIRE REPAIR PRIOR TO ADDITIONAL PLACEMENT. 6. MECHANICAL INTERLOCK METHODOLOGY IS NOT APPROPRIATE DUE TO POOR DURABILITY OF SITE WON SANDSTONE. FILL COMPOSITION IS REQUIRED TO INCLUDE AN APPROPRIATE SAND GRAVEL AND FINES COMPONENT CONFORMING TO THE REQUIREMENTS OF AS798. <p>KEY OUTCOMES FOR EARTHWORKS OPERATIONS</p> <ol style="list-style-type: none"> 1. DELIVER RESIDENTIAL LOTS WITH FAVOURABLE LOT CLASSIFICATIONS - I.E - NO P CLASSIFICATIONS 2. FILL THICKNESS DOES NOT VARY MORE THAN 2m OVER A DISTANCE OF 10m 3. CONSTRUCT FILL AND LIMIT LONG TERM CREEP SETTLEMENTS TO WITHIN 0.5% TO 1.0% OF THE FILL THICKNESS 4. BUILDING PLATFORM THAT ALLOWS BUILDERS TO CONSTRUCT SLAB ON GROUND RAFTS USING LIGHT EARTHMOVING EQUIPMENT 5. MATERIAL WON FROM CUTS AND USED IN FILL WITH REQUIRE: <ul style="list-style-type: none"> • CUTS IN ROCK AS WELL AS BLENDED WITH • CUTS IN FINER MATERIALS SUCH AS SANDS AND CLAYS 6. CREATING A FILL PLATFORM THAT IS ABLE TO BE TESTED IN ACCORDANCE WITH AS3798 AND AS1289 						

Lots and pavements where rock of medium strength or stronger was exposed at the final cut earthworks levels, were cut to a depth of approximately 0.6m below the final earthworks levels. The excavated rock was then replaced with fill materials compliant with the specification requirements for materials within the 0.0m to 0.6m depth range as described in Figure 4 and compacted accordingly.

3.0 METHODOLOGY

Earthworks Inspections and Testing was carried out on the stripped and exposed ground surfaces and during the placement and compaction of fill materials forming residential allotments and road subgrades.

Field and laboratory testing included walk over assessments of the existing ground conditions, proof roll testing of the stripped surface including the natural surface, observations of filling and compaction activities, field density testing using a soil moisture density gauge and Hilf Density compactions.

3.1 Stripped Surface Assessment

The fill areas covered by this report were stripped and cleared of visible loose materials, vegetation, and topsoil.

Materials exposed after stripping and that formed the fill foundation can be broadly summarised as:

- Natural - Silty Sand (SM) – at least dense, fine to medium grained sands, traces of low plasticity fines, grey – brown and moist.
- Natural – Sandy Clay (CI) – at least very stiff, medium plasticity, fine to medium grained sand, pale brown mottled orange and moist.
- Bedrock – Sandstone (XW-HW) – Extremely to Highly weathered, very low to low strength, orange – yellow brown

Following the stripped surface assessment of the fill areas, the foundation was approved for filling using the following process:

- Walk over assessments confirming that a competent natural foundation had been exposed.
- Proof roll testing using a large sized truck carrying out multiple passes confirming no movement of the exposed natural foundation.

A photo showing the showing a typical stripped surface is given in Picture 1.

Picture 1: View of The Site During Stripping Operations



3.2 Filling Operations

Fill materials were sourced onsite and can be broadly summarised as:

- Onsite Gravelly Sandy Clay (CI), medium plasticity fines, fine to coarse sand, fine to coarse gravel, yellow - brown and moist.
- Ripped Sandstone with engineering properties of Clayey Sandy Gravel (GC), fine to coarse sand, fine to coarse gravel, low to medium plasticity fines with cobbles up to 200mm max.
- Blasted Sandstone with engineering properties of Clayey Sandy Gravel (GC), fine to coarse sand, fine to coarse gravel, low to medium plasticity fines with cobbles up to 200mm max.

Ripping operations were required to loosen high and very high strength sandstone. Ripped rock was then processed using mechanical crushing plant.

The methodology for the rock crushing operations can be broadly summarised as: -

- Large rock fragments were broken down by an excavator with a hammer attachment to sizes acceptable for the mechanical crushing plant.
- Mechanical crushing to reduce rock fragments to 200mm size or less.
- Mixing crushed product with onsite materials using a front-end loader and placed into stockpiles assessed to be suitable for filling and earthworks operations.

Placement and compaction of the fill materials was carried out using the following plant:

- | | | |
|-------------------|--------------------|-----------------------------|
| • Water Carts | • Excavators | • Cat 825 Compactor |
| • Pad Foot Roller | • Grader | • Articulated Dump Truck's |
| • Dozers | • Front End Loader | • Mechanical Rock Crusher's |

The fill materials were moisture conditioned at the fill source and during placement to moisture contents suitable for compaction. Deleterious materials such as organics, sticks, roots and over size particles were sorted and removed during placement or were rejected for use. Occasional oversize particles including cobbles may be present in the deeper fill profile, however, are not considered to affect the fill as a mass.

Placement of the fill materials was carried out in layers appropriate for the above plant and compacted using the above plant carrying out multiple passes.

Our representative observed the filling process as described above which was assessed to be consistent for the entire thickness of fill.

Field density tests and laboratory compactions were carried out on the fill materials in accordance with Table 5.1 and 8.1 of AS3798 2007 (Guidelines on Earthworks for Commercial and Residential Developments) and tested to AS1289 test methods (Testing of Soils for Engineering Purposes).

Testing achieved the required specification of 95% of the maximum Hilf Density at the test locations.

Fill placed and compacted at measured density ratios less than 95% was tyned, moisture conditioned and re-compacted until the required specification was achieved. Retesting was carried out using the Random Stratified Location method.

The Location of the field density tests are shown on the Site Plan contained in Appendix A. These test locations and levels were not obtained by survey and therefore should only be considered as approximate.

Photos showing the typical fill construction activities are given in Pictures 2 to 4.

Picture 2: View of the Crushing Operation and Produced Product



Picture 3: View of the Site During Construction



Picture 4: View of the Site During Construction



4.0 STATEMENT OF COMPLIANCE

Our representatives observed the relevant earthworks operations including the stripped surface, fill placement and compaction operations and carried out field density tests and laboratory compaction tests in accordance with the required standards (AS3798, AS1289). Testing achieved the required specification of 95% Standard Maximum Dry Density (SMDD) at the test locations.

Level One Inspection and Testing has been carried out on the filling operation at the Site (limited to the extent shown in Figure 1). Based on the observations made by our Geo-technicians and the results of the field and laboratory tests, the placed and compacted fill at the above project has, as far as we have been able to assess, been constructed in general accordance with the intent of AS3798.

The fill can be deemed to be “controlled” in accordance with AS2870-2011 Residential Slabs and Footings.

5.0 EXCLUSIONS

This statement does not include any topsoil, which may be placed for use as dressing, trench backfill, areas outside the locations shown in Figure 1 or any other subsequent earthworks after 27 July 2023.

Assessments of material quality such as soaked CBR and site classifications are excluded from this commission.

Our on-site attendance specifically excludes assessments of fill material quality and engineering properties that are outside the requirements of AS3798 – 2007.

Footings and ground slabs for any structures constructed over natural soils or controlled fill should be designed to accommodate the characteristic ground surface movements and settlement potential. Assessments of these design parameters are beyond the scope of this Report.

6.0 LIMITATIONS

This Report has been prepared by Morrison Geotechnic (**Morrison Geotechnic**) and may include contributions from Morrison Geotechnic’s officers and employees, sub-contractors, sub-consultants or agents (**Contributors**).

This Report is for the sole benefit and use of Shadforth Civil Pty Ltd (**Client**), its designers, clients, and relevant statutory authorities for the sole purpose of providing geotechnical advice and recommendations in respect of the Bulk Earthworks Filling Operations at Precinct 10.2, Everleigh Estate (**Project**). The Report is only intended to address those issues expressly described in the Brief/ Work Instructions in this Report.

This Report should not be used or relied upon for any other purpose without Morrison Geotechnic’s prior written consent. Morrison Geotechnic and the Contributors do not accept any responsibility or liability in any way whatsoever for the use or reliance of this Report by anyone other than Golding Urban Pty Ltd (**Client**), its designers, its clients and relevant statutory authorities or by anyone else for any purpose other than that for which it has been prepared.

Except with Morrison Geotechnic’s prior written consent, this Report may not be:

- (a) released to any other party, whether in whole or in part (other than to the Client’s officers, employees, advisers, designers, clients and relevant statutory authorities);
- (b) used or relied upon by any other party.

Morrison Geotechnic and the Contributors do not accept any liability or responsibility whatsoever for, or in respect of, any use or reliance upon this Report by any other party. Morrison Geotechnic is not obliged to enter into discussions with any third party in respect of this Report.

The information (including technical information and information obtained through discussions) on which this report is based has been provided by the Client and third parties. Morrison Geotechnic and the Contributors:

- (a) have relied upon and presumed the accuracy of this information.
- (b) have not verified the accuracy or reliability of this information (other than as expressly stated in this Report).
- (c) have not made any independent investigations or enquiries in respect of those matters of which it has no actual knowledge at the time of giving this Report to the Client; and
- (d) make no warranty or guarantee, expressed or implied, as to the accuracy or reliability of this information.

Morrison Geotechnic and the Contributors do not accept responsibility or liability for any incorrect assumptions related to this Report. For the avoidance of doubt, this Report:

- (a) is not an environmental, contamination or hazardous materials assessment; may be invalid, incomplete or inaccurate (including errors in the scope of work, investigation methodology, observations, opinions and advice) where the information provided to Morrison Geotechnic was invalid, incomplete or inaccurate.
- (b) is limited to observations of those parts of the site described in Section 1.0.

No warranty or guarantee, whether express or implied, is made in respect of the geotechnical data, information, advice, opinions and recommendations present in this Report.

If further information becomes available, or additional assumptions need to be made, Morrison Geotechnic reserves its right to amend this Report.

If you have any queries regarding the above, please contact our office.

Yours faithfully



GARY TAYLOR
For and on behalf of
MORRISON GEOTECHNIC



SIMON WYNNE (RPEQ 17390)
For and on behalf of
MORRISON GEOTECHNIC

ATTACHMENTS:

- Appendix A – Site Plans Showing Test Locations
- Appendix B – Laboratory Test Results Reports



Appendix A

Site Plan & Test Locations

MORRISON GEOTECHNIC





LEGEND - PROPOSED

- NO CHANGES TO BULK EARTHWORKS. EARTHWORKS DONE AS PART OF PRECINCT 10.1 EARTHWORKS PACKAGE
- EXTENT OF CUT
- EXTENT OF FILL
- FINISHED MAJOR CONTOURS (1.00m)
- FINISHED MINOR CONTOURS (0.25m)
- 51.65 FINISHED SURFACE LEVEL
- H1.0 PROPOSED CONCRETE SLEEPER RETAINING WALL (AND HEIGHT). TIMBER TEXTURED SLEEPERS AND 2 COAT PAINT. DESIGN SPECIFICATION BY MANUFACTURER
- H1.0 PROPOSED CONCRETE PANEL RETAINING WALL (AND HEIGHT). 2 COAT TEXTURED PAINT. DESIGN SPECIFICATION BY MANUFACTURER
- FEATURE FENCE ON TOP OF RETAINING WALL BY LANDSCAPER
- 58.25 X FOOTPATH SPOT LEVEL
- ZERO LOT LINE
- ↓ PROPOSED FUTURE DRIVEWAY LOCATION
- STAGE BOUNDARY

LEGEND - CONSTRUCTED


- RETAINING WALL
- CONTOURS (0.50m)
- SW STORMWATER
- S SEWER
- W WATER

- NOTES**
1. REFER TO BULK EARTHWORKS NOTES & DETAILS DRAWINGS FOR:
 - EARTHWORKS NOTES AND DETAILS
 - RETAINING WALL NOTES AND DETAILS
 2. PROPOSED SERVICES ARE WITHIN THE VICINITY OF RETAINING WALLS. REFER SERVICE DRAWINGS FOR SERVICE LOCATIONS AND DETAILS.
 3. EXISTING DWELLINGS, FENCES ETC TO BE DEMOLISHED AND REMOVED OFF SITE BY OTHERS (UNLESS NOTED OTHERWISE)
 4. FINAL RETAINING WALL TYPES AND FINISHES SHALL BE CONFIRMED WITH THE SUPERINTENDENT PRIOR TO CONSTRUCTION.

LAYOUT PLAN
SCALE 1:500

EARTHWORKS FOR LOTS 4011-4012, 4017-4018, 4039-4044 & 4076-4094 COMPLETED AS PART OF PRECINCT 9 & 10.1 WORKS

FOR CONSTRUCTION			<p>BRISBANE OFFICE LEVEL 11, 300 ADELAIDE STREET BRISBANE, QLD 4000 PH: (07) 3253 2222 WEB: www.premise.com.au</p>	<p>DESIGNED KLYNT KIWANG</p> <p>CHECKED ANDREW LANGDON</p> <p>PROJECT MANAGER NICK SOMERVILLE</p> <p>PROJECT DIRECTOR <i>[Signature]</i> PATRICK BRADY RPEQ 7112</p>	<p>SCALE</p> <p>SCALE 1:500 (A1)</p> <p>ORIGINAL SHEET SIZE A1</p>	<p>CLIENT MIRVAC QLD PTY LTD</p>		<p>JOB CODE MIR-1002</p>
						<p>PROJECT EVERLEIGH PRECINCT 10.2 SUBDIVISION DEVELOPMENT</p>		
			<p>SHEET TITLE BULK EARTHWORKS LAYOUT PLAN - SHEET 1</p>		<p>SHEET NUMBER C200</p>		<p>REV B</p>	
07/12/2023	B	ISSUED FOR CONSTRUCTION - UPDATED PAD LEVELS AND RETAINING WALL HEIGHTS	KK	PB				
09/05/2023	A	ISSUED FOR APPROVAL	KK	PB				
DATE	REV	DESCRIPTION	REC	APP	REVISIONS			

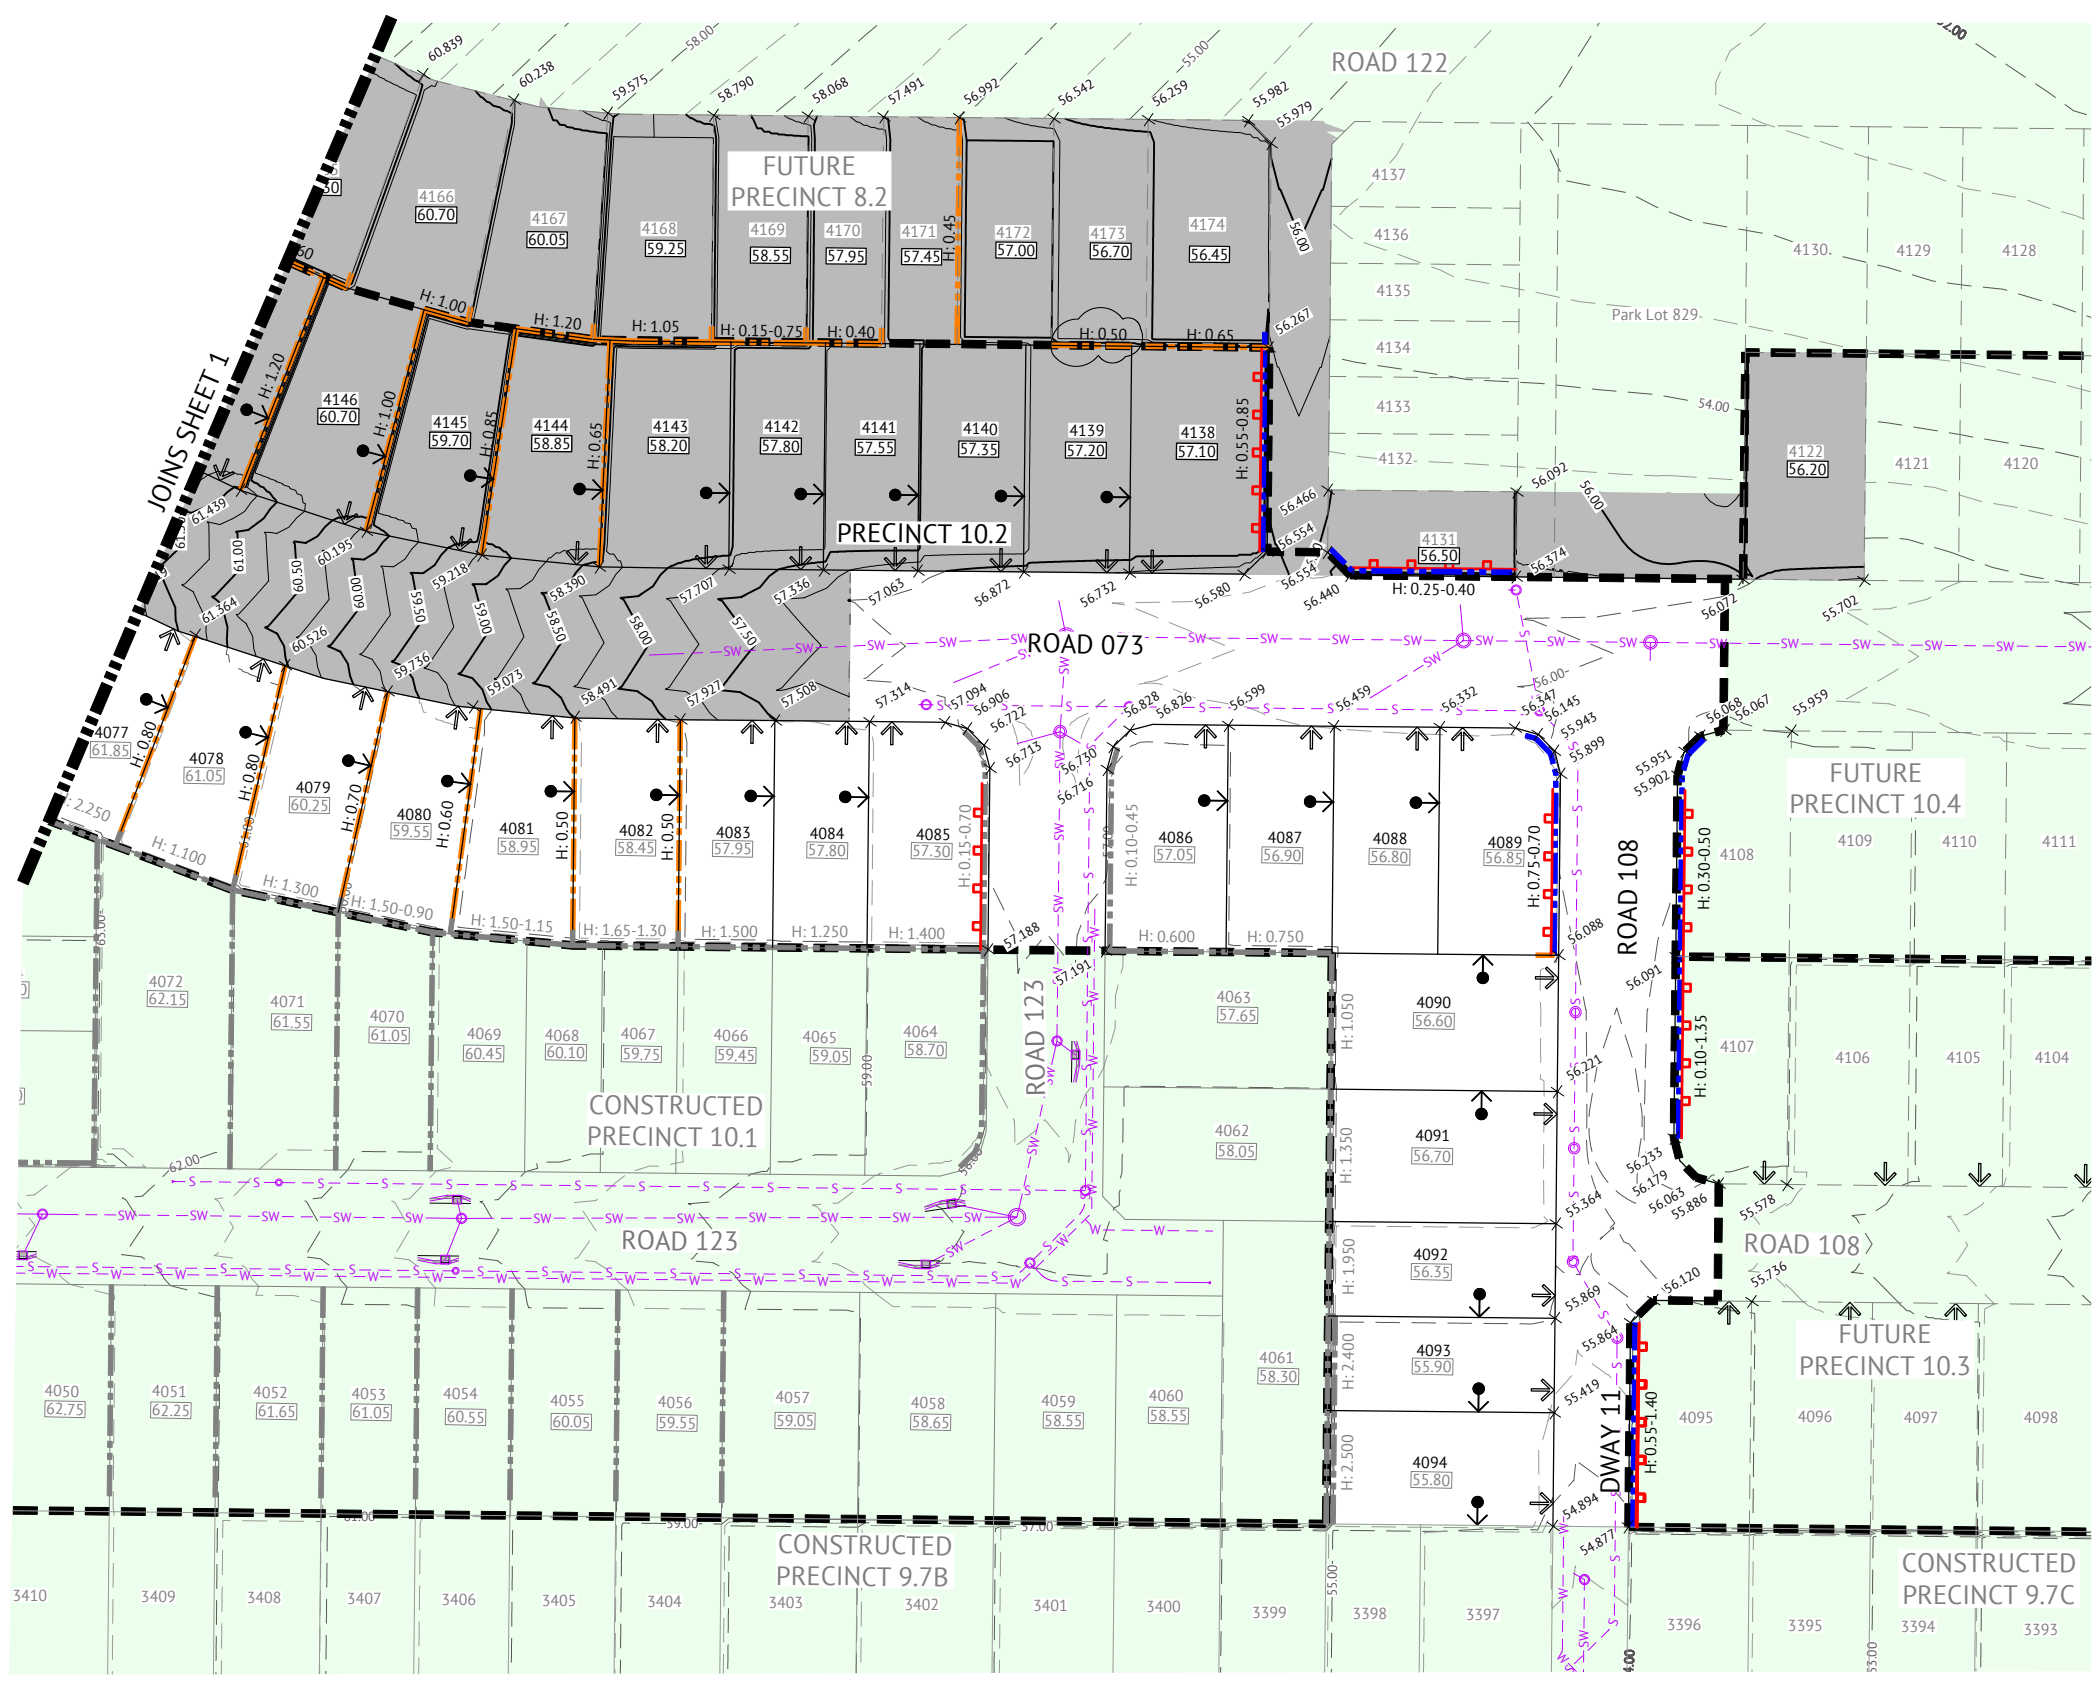


- LEGEND - PROPOSED**
- NO CHANGES TO BULK EARTHWORKS. EARTHWORKS DONE AS PART OF PRECINCT 10.1 EARTHWORKS PACKAGE
 - EXTENT OF CUT
 - EXTENT OF FILL
 - FINISHED MAJOR CONTOURS (1.00m)
 - FINISHED MINOR CONTOURS (0.25m)
 - 51.65 FINISHED SURFACE LEVEL
 - PROPOSED CONCRETE SLEEPER RETAINING WALL (AND HEIGHT). TIMBER TEXTURED SLEEPERS AND 2 COAT PAINT. DESIGN SPECIFICATION BY MANUFACTURER
 - PROPOSED CONCRETE PANEL RETAINING WALL (AND HEIGHT). 2 COAT TEXTURED PAINT. DESIGN SPECIFICATION BY MANUFACTURER
 - FEATURE FENCE ON TOP OF RETAINING WALL BY LANDSCAPER
 - 58.25 X FOOTPATH SPOT LEVEL
 - ZERO LOT LINE
 - ↓ PROPOSED FUTURE DRIVEWAY LOCATION
 - STAGE BOUNDARY

- LEGEND - CONSTRUCTED**
- RETAINING WALL
 - CONTOURS (0.50m)
 - STORMWATER
 - SEWER
 - WATER

LAYOUT PLAN
SCALE 1:500

EARTHWORKS FOR LOTS 4011-4012, 4017-4018, 4039-4044 & 4076-4094 COMPLETED AS PART OF PRECINCT 9 & 10.1 WORKS

FOR CONSTRUCTION			 BRISBANE OFFICE LEVEL 11, 300 ADELAIDE STREET BRISBANE, QLD 4000 PH: (07) 3253 2222 WEB: www.premise.com.au	DESIGNED KLYNT KIWANG CHECKED ANDREW LANGDON PROJECT MANAGER NICK SOMERVILLE PROJECT DIRECTOR PATRICK BRADY RPEQ 7112	SCALE SCALE 1:500 (A1) ORIGINAL SHEET SIZE A1	CLIENT MIRVAC QLD PTY LTD		JOB CODE MIR-1002
PROJECT EVERLEIGH PRECINCT 10.2 SUBDIVISION DEVELOPMENT						LOCATION TEVIOT ROAD, GREENBANK		
07/12/2023	B	ISSUED FOR CONSTRUCTION - ADDED RETAINING WALL	KK	PB				
09/05/2023	A	ISSUED FOR APPROVAL	KK	PB				
DATE	REV	DESCRIPTION	REC	APP				
REVISIONS								
			SHEET NUMBER C201		REV B			

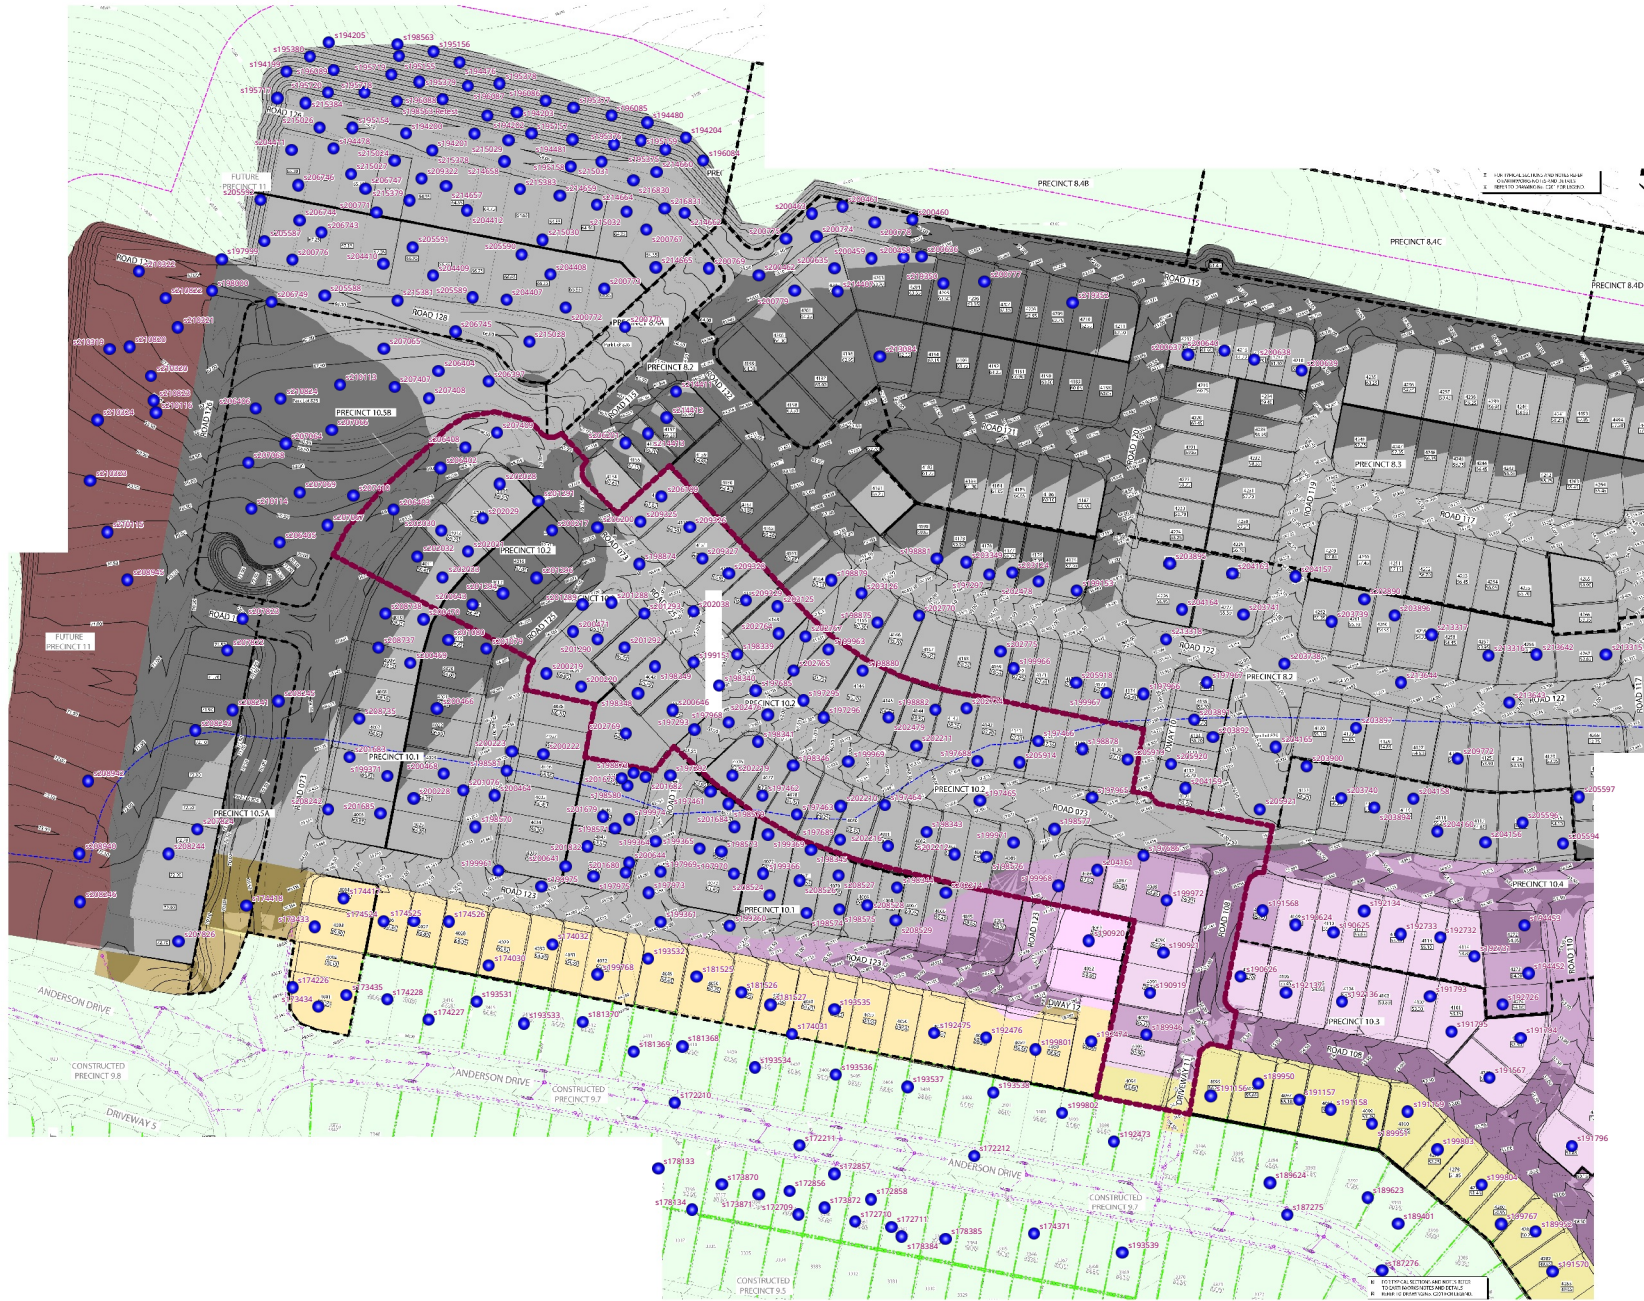

EVERLEIGH PRECINCT 10.2 - LEVEL 1 TESTS



Appendix B



Laboratory Test Reports

MORRISON GEOTECHNIC





MORRISON
GEOTECHNIC



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/11755 - 11/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	6/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 1 of 1		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/197292	S/197293	S/197294	S/197295	S/197296	S/197297
Date Tested :	23/05/2023	23/05/2023	23/05/2023	23/05/2023	23/05/2023	23/05/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	10:00	10:15	10:30	10:45	11:00	11:15
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499135	E 499145	E 499165	E 499180	E 499198	E 499219
Location 2 :	N 6932280	N 6932299	N 6932302	N 6932303	N 6932304	N 6932306
Location 3 :	RL 2.9	RL 3.0	RL 2.8	RL 2.8	RL 2.7	RL 2.6
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/197292	S/197293	S/197294	S/197295	S/197296	S/197297
MDR Test Date :	26/05/2023	26/05/2023	26/05/2023	26/05/2023	26/05/2023	26/05/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.13	2.13	2.13	2.13	2.13	2.13
Moisture Variation :	-1.0%	-1.0%	-1.0%	-1.0%	-1.0%	-1.0%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	15.5%	13.0%	10.5%	10.0%	16.5%	9.5%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	1.0% Wet of OMC	1.0% Wet of OMC	1.0% Wet of OMC	1.0% Wet of OMC	1.0% Wet of OMC	1.0% Wet of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.08	2.08	2.09	2.09	2.10	2.09
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	98.0%	98.0%	98.0%	98.0%	98.5%	98.0%
Remarks :						
 <p>Accredited for Compliance with ISO / IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast</p> <p>Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>		



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth 99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Number :	SR/PTP/11755 - 12/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	6/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 1 of 1		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/197684	S/197685	S/197686	S/197687	S/197688	S/197689
Date Tested :	25/05/2023	25/05/2023	25/05/2023	25/05/2023	25/05/2023	25/05/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	10:10	10:20	10:30	10:40	10:50	11:00
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499135	E 499170	E 499217	E 499248	E 499215	E 499195
Location 2 :	N 6932300	N 6932315	N 6932330	N 6932297	N 6932277	N 6932257
Location 3 :	RL 58.6	RL 58.2	RL 58.6	RL 58.0	RL 58.2	RL 58.3
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/197684	S/197685	S/197686	S/197687	S/197688	S/197689
MDR Test Date :	29/05/2023	29/05/2023	29/05/2023	29/05/2023	29/05/2023	29/05/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.02	2.10	2.01	2.03	2.00	1.99
Moisture Variation :	1.5%	2.0%	2.0%	2.0%	2.5%	2.0%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	15.0%	14.5%	14.0%	15.5%	15.0%	32.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	1.5% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.5% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.01	2.01	2.00	2.03	1.99	1.99
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	99.0%	96.0%	99.0%	100.0%	99.5%	99.5%
Remarks :						
 <p>Accredited for Compliance with ISO / IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  Nick Dobson - Signatory		



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/11755 - 13/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	6/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 1 of 2		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/197965	S/197966	S/197967	S/197968	S/197969	S/197970
Date Tested :	26/05/2023	26/05/2023	26/05/2023	26/05/2023	26/05/2023	26/05/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	09:15	09:30	09:45	10:00	10:15	10:30
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499308	E 499324	E 499359	E 499150	E 499133	E 499161
Location 2 :	N 6932271	N 6932304	N 6932315	N 6932308	N 6932248	N 6932240
Location 3 :	RL 58.5	RL 58.3	RL 58.1	RL 58.0	RL 58.7	RL 58.7
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/197965	S/197966	S/197967	S/197968	S/197969	S/197970
MDR Test Date :	30/05/2023	30/05/2023	30/05/2023	30/05/2023	30/05/2023	30/05/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.09	2.11	2.12	2.08	2.03	2.15
Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.0%	2.0%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	9.5%	9.0%	9.5%	9.5%	9.0%	10.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.01	2.00	2.01	2.00	1.93	2.09
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	96.0%	95.0%	95.0%	95.5%	95.0%	97.5%
Remarks :						
 <p>Accredited for Compliance with ISO / IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  Nick Dobson - Signatory		



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth 99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Number :	SR/PTP/11755 - 15/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	12/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 1 of 2		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/198338	S/198339	S/198340	S/198341	S/198342	S/198343
Date Tested :	29/05/2023	29/05/2023	29/05/2023	29/05/2023	29/05/2023	29/05/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	09:00	09:15	09:30	09:45	10:00	10:15
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499244	E 499188	E 499155	E 499171	E 499189	E 499240
Location 2 :	N 6932330	N 6932329	N 6932317	N 6932294	N 6932268	N 6932257
Location 3 :	RL 59.2	RL 59.4	RL 59.5	RL 58.7	RL 58.6	RL 58.6
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/198338	S/198339	S/198340	S/198341	S/198342	S/198343
MDR Test Date :	1/06/2023	1/06/2023	1/06/2023	1/06/2023	1/06/2023	1/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Gravelly SAND - Dark Brown	Gravelly SAND - Light Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.02	2.09	2.05	2.07	2.06	2.07
Moisture Variation :	2.0%	1.5%	2.0%	2.0%	1.0%	2.0%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	6.5%	7.5%	11.5%	10.5%	10.5%	12.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	1.5% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	1.0% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	1.98	1.99	1.99	1.98	1.99	2.01
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	97.5%	95.0%	97.0%	95.5%	97.0%	96.5%
Remarks :						
 <p>Accredited for Compliance with ISO/IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  Nick Dobson - Signatory		



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth 99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Number :	SR/PTP/11755 - 15/1	
Client Address :	Everleigh Precinct 8 and 10 BEW - LV1			Report Date :	12/06/2023	
Project Name :	PTP/11755			Test Request :	-	
Project Number :				Page 2 of 2		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/198344	S/198345	S/198346	S/198347	S/198348	S/198349
Date Tested :	29/05/2023	29/05/2023	29/05/2023	29/05/2023	29/05/2023	29/05/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	10:30	10:45	11:00	11:15	11:30	11:41
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499228	E 499194	E 499169	E 499147	E 499105	E 499107
Location 2 :	N 6932234	N 6932251	N 6932277	N 6932303	N 6932324	N 6932336
Location 3 :	RL 59.8	RL 60.2	RL 60.4	RL 64.05	RL 60.64	RL 64.05
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	7%	12%	10%	6%	17%	19%
Oversize Density - Dry (t/m ³) :	2.34	2.11	2.19	2.34	2.23	2.13
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/198344	S/198345	S/198346	S/198347	S/198348	S/198349
MDR Test Date :	1/06/2023	1/06/2023	1/06/2023	1/06/2023	1/06/2023	1/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.03	2.21	1.97	2.04	1.98	1.97
Moisture Variation :	1.0%	1.0%	1.5%	2.0%	1.5%	1.5%
ADJ PCWD (t/m ³) :	2.05	2.20	1.99	2.05	2.02	2.00
ADJ Moisture Variation :	1.0%	0.5%	1.5%	1.5%	1.5%	1.0%
<i>Moisture Test Results :</i>						
Field Moisture Content :	10.5%	9.5%	9.5%	8.0%	10.0%	9.5%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	1.0% Dry of OMC	0.5% Dry of OMC	1.5% Dry of OMC	1.5% Dry of OMC	1.5% Dry of OMC	1.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	1.95	2.22	1.95	1.95	1.93	1.95
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	95.0%	101.0%	97.5%	95.0%	95.5%	97.5%
Remarks :						
 <p>Accredited for Compliance with ISO / IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>		



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth 99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Number :	SR/PTP/11755 - 16/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	12/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 2 of 2		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/198576	S/198577	S/198578	S/198579	S/198580	S/198581
Date Tested :	30/05/2023	30/05/2023	30/05/2023	30/05/2023	30/05/2023	30/05/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	09:15	09:30	09:45	10:00	10:15	10:30
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499261	E 499288	E 499194	E 499159	E 499115	E 499068
Location 2 :	N 6932254	N 6932261	N 6932266	N 6932271	N 6932276	N 6932282
Location 3 :	RL 59.4	RL 59.4	RL 59.6	RL 59.6	RL 59.7	RL 59.7
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/198576	S/198577	S/198578	S/198579	S/198580	S/198581
MDR Test Date :	2/06/2023	2/06/2023	2/06/2023	2/06/2023	2/06/2023	2/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Sandy CLAY - Light Brown	Sandy CLAY - Light Brown	Sandy CLAY - Light Brown	Sandy CLAY - Light Brown	Sandy CLAY - Light Brown	Sandy CLAY - Light Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	1.99	1.99	1.98	1.99	1.99	1.99
Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.0%	2.0%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	9.0%	10.0%	9.5%	9.5%	10.0%	10.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	1.96	1.96	1.96	1.97	1.98	1.97
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	98.5%	99.0%	99.0%	99.0%	99.5%	99.0%
Remarks :						
 <p>Accredited for Compliance with ISO/IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast</p> <p>Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  Nick Dobson - Signatory		



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/11755 - 17/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	12/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 1 of 2		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/198873	S/198874	S/198875	S/198876	S/198877	S/198878
Date Tested :	31/05/2023	31/05/2023	31/05/2023	31/05/2023	31/05/2023	31/05/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	09:00	09:15	09:30	10:00	10:15	10:30
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499115	E 499138	E 499220	E 499250	E 499290	E 499304
Location 2 :	N 6933280	N 6932361	N 6932343	N 6932341	N 6932333	N 6932291
Location 3 :	RL 63.15	RL 63.1	RL 63.1	RL 63.0	RL 59.21	RL 58.5
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/198873	S/198874	S/198875	S/198876	S/198877	S/198878
MDR Test Date :	5/06/2023	5/06/2023	5/06/2023	5/06/2023	5/06/2023	5/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.01	2.01	2.01	2.02	2.02	2.02
Moisture Variation :	0.5%	0.5%	0.5%	0.5%	0.5%	0.5%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	12.5%	11.0%	12.0%	10.5%	16.5%	14.5%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	0.5% Dry of OMC	0.5% Dry of OMC	0.5% Dry of OMC	0.5% Dry of OMC	0.5% Dry of OMC	0.5% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.00	1.99	2.01	1.99	2.01	2.00
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	99.5%	99.0%	100.0%	98.5%	99.5%	99.0%
Remarks :						
 <p>Accredited for Compliance with ISO/IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  Nick Dobson - Signatory		


Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/11755 - 17/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	12/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 2 of 2		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/198879	S/198880	S/198881	S/198882	S/198883	S/198884
Date Tested :	31/05/2023	31/05/2023	31/05/2023	31/05/2023	31/05/2023	31/05/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	10:45	11:00	11:15	11:30	11:45	12:00
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499193	E 499214	E 499238	E 499254	E 499268	E 499290
Location 2 :	N 6932329	N 6932323	N 6932321	N 6932316	N 6932320	N 6932320
Location 3 :	RL 59.2	RL 59.2	RL 59.2	RL 59.2	RL 59.3	RL 59.4
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	15%	18%	18%	15%	18%	17%
Oversize Density - Dry (t/m ³) :	2.14	2.13	2.18	2.12	2.14	2.11
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/198879	S/198880	S/198881	S/198882	S/198883	S/198884
MDR Test Date :	5/06/2023	5/06/2023	5/06/2023	5/06/2023	5/06/2023	5/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	1.95	2.02	1.94	2.01	1.95	1.97
Moisture Variation :	1.0%	1.0%	2.5%	0.5%	2.5%	2.5%
ADJ PCWD (t/m ³) :	1.97	2.04	1.98	2.03	1.98	1.99
ADJ Moisture Variation :	1.0%	0.5%	2.0%	0.5%	2.0%	2.0%
<i>Moisture Test Results :</i>						
Field Moisture Content :	12.0%	10.0%	9.5%	11.5%	9.5%	10.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	1.0% Dry of OMC	0.5% Dry of OMC	2.0% Dry of OMC	0.5% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	1.94	2.00	2.00	2.00	2.00	1.99
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	98.5%	98.0%	101.0%	98.5%	100.5%	100.0%
Remarks :						
 <p>Accredited for Compliance with ISO/IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast</p> <p>Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>		



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth 99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Number :	SR/PTP/11755 - 18/1	
Client Address :	Everleigh Precinct 8 and 10 BEW - LV1			Report Date :	12/06/2023	
Project Name :	PTP/11755			Test Request :	-	
Project Number :				Page 1 of 1		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/199151	S/199152	S/199153	S/199154	S/199155	S/199156
Date Tested :	1/06/2023	1/06/2023	1/06/2023	1/06/2023	1/06/2023	1/06/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	10:00	10:15	10:30	10:45	11:00	11:15
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499147	E 499180	E 499206	E 499237	E 499270	E 499292
Location 2 :	N 6932300	N 6932296	N 6932297	N 6932291	N 6932292	N 6932295
Location 3 :	RL 61.1	RL 61.1	RL 59.4	RL 59.4	RL 57.9	RL 57.9
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/199151	S/199152	S/199153	S/199154	S/199155	S/199156
MDR Test Date :	5/06/2023	5/06/2023	5/06/2023	5/06/2023	5/06/2023	5/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Gravelly Clayey SAND Brown	Gravelly Clayey SAND Brown	Gravelly Clayey SAND Brown	Gravelly Clayey SAND Brown	Gravelly Clayey SAND Brown	Gravelly Clayey SAND Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.04	2.01	2.02	2.09	2.08	2.09
Moisture Variation :	2.0%	2.0%	2.0%	1.5%	2.0%	1.0%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	12.0%	12.0%	12.0%	11.5%	11.5%	12.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	1.5% Dry of OMC	2.0% Dry of OMC	1.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	1.99	1.99	2.08	2.10	2.11	2.10
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	97.5%	99.0%	102.5%	100.5%	101.5%	100.5%
Remarks :						
 <p>Accredited for Compliance with ISO/IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  Nick Dobson - Signatory		



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth						Report Number :	SR/PTP/11755 - 20/1
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD						Report Date :	13/06/2023
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1						Test Request :	-
Project Number :	PTP/11755						Page 1 of 3	
Location :	Lyons							
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,							
Sample Number :	S/199961	S/199962	S/199963	S/199964	S/199965	S/199966		
Date Tested :	7/06/2023	7/06/2023	7/06/2023	7/06/2023	7/06/2023	7/06/2023		
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite		
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill		
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175		
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b		
Time :	10:00	10:10	10:20	10:30	10:40	10:50		
Lot Number :	-	-	-	-	-	-		
Location 1 :	E 499081	E 499188	E 499200	E 499253	E 499280	E 499276		
Location 2 :	N 6932244	N 6932246	N 6932332	N 6932255	N 6932299	N 6932324		
Location 3 :	RL 65.42	RL 65.30	RL 65.37	RL 65.47	RL 65.40	RL 65.44		
Location 4 :	-	-	-	-	-	-		
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm		
Oversize Wet :	18%	16%	13%	16%	15%	13%		
Oversize Density - Dry (t/m ³) :	2.38	2.37	2.39	2.41	2.40	2.43		
Assigned MDR (Yes/No) :	No	No	No	No	No	No		
MDR Sample Number :	S/199961	S/199962	S/199963	S/199964	S/199965	S/199966		
MDR Test Date :	12/06/2023	12/06/2023	12/06/2023	12/06/2023	12/06/2023	12/06/2023		
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard		
Soil Description :	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown		
MDR Test Results								
PCWD (t/m ³) :	2.01	2.02	2.02	2.01	2.03	2.03		
Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.5%	2.0%		
ADJ PCWD (t/m ³) :	2.07	2.07	2.06	2.07	2.08	2.07		
ADJ Moisture Variation :	1.5%	1.5%	1.5%	2.0%	2.0%	1.5%		
Moisture Test Results :								
Field Moisture Content :	8.5%	9.0%	9.5%	9.0%	9.0%	10.0%		
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC		
Variation from OMC :	1.5% Dry of OMC	1.5% Dry of OMC	1.5% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	1.5% Dry of OMC		
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-		
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A		
Density Test Results								
Field Wet Density (t/m ³) :	2.03	2.08	2.04	2.05	2.02	2.03		
Density Specification :	95%	95%	95%	95%	95%	95%		
Wet Density Ratio :	98.0%	100.0%	99.0%	99.5%	97.0%	97.5%		
Remarks :								
 <p>Accredited for Compliance with ISO/ IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				APPROVED SIGNATORY  Nick Dobson - Signatory				



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth					Report Number :	SR/PTP/11755 - 20/1
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD					Report Date :	13/06/2023
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1					Test Request :	-
Project Number :	PTP/11755					Page 2 of 3	
Location :	Lyons						
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,						
Sample Number :	S/199967	S/199968	S/199969	S/199970	S/199971	S/199972	
Date Tested :	7/06/2023	7/06/2023	7/06/2023	7/06/2023	7/06/2023	7/06/2023	
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite	
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill	
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	
Time :	11:00	11:10	11:20	11:30	11:40	11:50	
Lot Number :	-	-	-	-	-	-	
Location 1 :	E 499314	E 499285	E 499208	E 499257	E 499284	E 499365	
Location 2 :	N 6932314	N 6932312	N 6932286	N 6932320	N 6932307	N 6932287	
Location 3 :	RL 65.38	RL 65.33	RL 65.36	RL 65.40	RL 64.98	RL 64.95	
Location 4 :	-	-	-	-	-	-	
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	
Oversize Wet :	14%	6%	4%	7%	0%	0%	
Oversize Density - Dry (t/m ³) :	2.13	2.06	2.04	2.10	-	-	
Assigned MDR (Yes/No) :	No	No	No	No	No	No	
MDR Sample Number :	S/199967	S/199968	S/199969	S/199970	S/199971	S/199972	
MDR Test Date :	12/06/2023	12/06/2023	12/06/2023	12/06/2023	12/06/2023	12/06/2023	
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard	
Soil Description :	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	
MDR Test Results							
PCWD (t/m ³) :	2.02	2.03	2.04	2.04	2.02	2.05	
Moisture Variation :	0.5%	1.5%	1.5%	2.0%	2.0%	2.0%	
ADJ PCWD (t/m ³) :	2.04	2.04	2.04	2.04	-	-	
ADJ Moisture Variation :	0.5%	1.0%	1.5%	2.0%	-	-	
Moisture Test Results :							
Field Moisture Content :	11.5%	13.5%	13.0%	11.0%	10.5%	11.5%	
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	
Variation from OMC :	0.5% Dry of OMC	1.0% Dry of OMC	1.5% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-	
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A	
Density Test Results							
Field Wet Density (t/m ³) :	1.95	1.94	1.99	2.07	1.97	2.00	
Density Specification :	95%	95%	95%	95%	95%	95%	
Wet Density Ratio :	95.5%	95.0%	98.0%	101.5%	97.5%	98.0%	
Remarks :							
 <p>Accredited for Compliance with ISO/ IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>			



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/11755 - 21/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	14/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 1 of 1		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/197461	S/197462	S/197463	S/197464	S/197465	S/197466
Date Tested :	24/05/2023	24/05/2023	24/05/2023	24/05/2023	24/05/2023	24/05/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	10:00	10:15	10:30	10:45	11:00	11:15
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499153	E 499164	E 499187	E 499223	E 499262	E 499287
Location 2 :	N 6932275	N 6932264	N 6932264	N 6932268	N 6932270	N 6932283
Location 3 :	RL 3.0	RL 2.9	RL 2.9	RL 2.7	RL 2.6	RL 2.6
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/197461	S/197462	S/197463	S/197464	S/197465	S/197466
MDR Test Date :	26/05/2023	26/05/2023	26/05/2023	26/05/2023	26/05/2023	26/05/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.04	2.04	2.01	2.06	2.03	2.05
Moisture Variation :	1.5%	2.0%	1.5%	2.0%	2.0%	1.5%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	13.5%	14.0%	13.5%	12.5%	12.0%	12.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	1.5% Dry of OMC	2.0% Dry of OMC	1.5% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	1.5% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.03	2.02	2.03	2.02	2.02	2.04
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	99.5%	99.0%	101.0%	98.0%	99.5%	99.5%
Remarks :						
 <p>Accredited for Compliance with ISO / IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast</p> <p>Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>		



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth 99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Number :	SR/PTP/11755 - 22/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	14/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 1 of 3		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/200214	S/200215	S/200216	S/200217	S/200218	S/200219
Date Tested :	8/06/2023	8/06/2023	8/06/2023	8/06/2023	8/06/2023	8/06/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	09:00	09:10	09:20	09:30	09:40	09:50
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499082	E 499042	E 499056	E 499095	E 499092	E 499082
Location 2 :	N 6932253	N 6932254	N 6932315	N 6932329	N 6932325	N 6932318
Location 3 :	RL 65.80	RL 65.94	RL 65.97	RL 66.12	RL 66.05	RL 66.11
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	7%	0%	7%	0%	0%
Oversize Density - Dry (t/m ³) :	-	2.19	-	2.22	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/200214	S/200215	S/200216	S/200217	S/200218	S/200219
MDR Test Date :	13/06/2023	13/06/2023	13/06/2023	13/06/2023	13/06/2023	13/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.02	2.05	2.02	2.00	2.01	2.01
Moisture Variation :	1.5%	2.0%	2.0%	2.0%	2.0%	1.5%
ADJ PCWD (t/m ³) :	-	2.06	-	2.02	-	-
ADJ Moisture Variation :	-	2.0%	-	2.0%	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	9.5%	9.0%	9.5%	9.0%	10.5%	10.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	1.5% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	1.5% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.02	2.01	2.04	2.05	2.00	2.04
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	100.0%	97.5%	100.5%	101.5%	100.0%	101.5%
Remarks :						
 <p>Accredited for Compliance with ISO/IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  Nick Dobson - Signatory		



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/11755 - 22/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	14/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 2 of 3		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/200220	S/200221	S/200222	S/200223	S/200224	S/200225
Date Tested :	8/06/2023	8/06/2023	8/06/2023	8/06/2023	8/06/2023	8/06/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	10:00	10:10	10:20	10:30	10:40	10:50
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499093	E 499079	E 499083	E 499070	E 499075	E 499061
Location 2 :	N 6932313	N 6932303	N 6932289	N 6932290	N 6932278	N 6932306
Location 3 :	RL 66.14	RL 65.99	RL 66.10	RL 66.14	RL 66.08	RL 66.20
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	3%	2%	0%	10%	7%	7%
Oversize Density - Dry (t/m ³) :	2.20	2.20	-	2.12	2.12	2.15
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/200220	S/200221	S/200222	S/200223	S/200224	S/200225
MDR Test Date :	13/06/2023	13/06/2023	13/06/2023	13/06/2023	13/06/2023	13/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown	Gravelly Sandy CLAY - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.04	2.05	2.09	2.03	2.05	2.04
Moisture Variation :	1.5%	2.0%	2.0%	2.0%	2.0%	2.0%
ADJ PCWD (t/m ³) :	2.05	2.05	-	2.04	2.05	2.05
ADJ Moisture Variation :	1.5%	2.0%	-	1.5%	1.5%	1.5%
<i>Moisture Test Results :</i>						
Field Moisture Content :	10.0%	10.0%	10.5%	8.0%	9.5%	10.5%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	1.5% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	1.5% Dry of OMC	1.5% Dry of OMC	1.5% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.03	2.02	2.10	2.08	2.05	2.03
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	99.0%	98.5%	100.5%	102.0%	99.5%	99.0%
Remarks :						
 <p>Accredited for Compliance with ISO/IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast</p> <p>Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>		



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/11755 - 23/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	22/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 3 of 3		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/200469	S/200470	S/200471			
Date Tested :	9/06/2023	9/06/2023	9/06/2023			
Material Source :	Onsite	Onsite	Onsite			
For use as :	General Fill	General Fill	General Fill			
Test / Layer Depths :	150 / 175	150 / 175	150 / 175			
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b			
Time :	11:40	11:50	12:00			
Lot Number :	-	-	-			
Location 1 :	E 499043	E 499060	E 499078			
Location 2 :	N 6932323	N 6932341	N 6932344			
Location 3 :	RL 66.09	RL 66.17	RL 66.12			
Location 4 :	-	-	-			
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm			
OverSize Wet :	0%	0%	0%			
OverSize Density - Dry (t/m ³) :	-	-	-			
Assigned MDR (Yes/No) :	No	No	No			
MDR Sample Number :	S/200469	S/200470	S/200471			
MDR Test Date :	14/06/2023	14/06/2023	14/06/2023			
Compaction Type :	Standard	Standard	Standard			
Soil Description :	Sandy Gravelly CLAY - Light Brown	Sandy Gravelly CLAY - Light Brown	Sandy Gravelly CLAY - Light Brown			
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.11	2.12	2.15			
Moisture Variation :	0.5%	0.5%	0.5%			
ADJ PCWD (t/m ³) :	-	-	-			
ADJ Moisture Variation :	-	-	-			
<i>Moisture Test Results :</i>						
Field Moisture Content :	15.0%	14.5%	14.5%			
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC			
Variation from OMC :	0.5% Dry of OMC	0.5% Dry of OMC	0.5% Dry of OMC			
Relative Moisture Ratio (Q250) :	-	-	-			
Moisture Ratio :	N/A	N/A	N/A			
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.07	2.06	2.05			
Density Specification :	95%	95%	95%			
Wet Density Ratio :	98.5%	97.0%	95.5%			
Remarks :						
 <p>Accredited for Compliance with ISO/IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  Nick Dobson - Signatory		



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/11755 - 26/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	22/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 1 of 1		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/200635	S/200636	S/200637	S/200638	S/200639	S/200640
Date Tested :	12/06/2023	12/06/2023	12/06/2023	12/06/2023	12/06/2023	12/06/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	10:00	10:15	10:30	10:45	11:00	11:15
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499197	E 499238	E 499282	E 499331	E 499456	E 499310
Location 2 :	N 6932493	N 6932493	N 6932487	N 6932477	N 6932488	N 6932495
Location 3 :	RL 63.3	RL 63.3	RL 63.3	RL 62.9	RL 62.9	RL 62.9
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/200635	S/200636	S/200637	S/200638	S/200639	S/200640
MDR Test Date :	15/06/2023	15/06/2023	15/06/2023	15/06/2023	15/06/2023	15/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.09	2.08	2.08	2.09	2.07	2.09
Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.0%	2.0%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	8.0%	8.0%	8.0%	8.0%	8.0%	7.5%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.00	2.00	2.02	2.01	2.02	2.02
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	96.0%	96.0%	97.0%	96.0%	97.5%	96.5%
Remarks :						
 <p>Accredited for Compliance with ISO/IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast</p> <p>Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  Nick Dobson - Signatory		



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth 99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Number :	SR/PTP/11755 - 30/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	22/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 1 of 2		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/201288	S/201289	S/201290	S/201291	S/201292	S/201293
Date Tested :	15/06/2023	15/06/2023	15/06/2023	15/06/2023	15/06/2023	15/06/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	08:30	08:50	09:00	09:10	09:20	09:30
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499111	E 499108	E 499105	E 499114	E 499108	E 499102
Location 2 :	N 6932351	N 6932341	N 6932336	N 6932339	N 6932334	N 6932330
Location 3 :	RL 66.81	RL 66.78	RL 66.69	RL 66.77	RL 66.74	RL 66.80
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/201288	S/201289	S/201290	S/201291	S/201292	S/201293
MDR Test Date :	20/06/2023	19/06/2023	20/06/2023	20/06/2023	20/06/2023	20/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.09	2.12	2.11	2.11	2.07	2.10
Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.0%	2.0%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	11.0%	11.0%	10.0%	11.5%	11.0%	11.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.11	2.14	2.13	2.14	2.09	2.11
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	101.0%	101.0%	100.5%	101.5%	101.0%	100.5%
Remarks :						
 <p>Accredited for Compliance with ISO/IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  Nick Dobson - Signatory		



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/11755 - 30/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	22/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 2 of 2		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/201294	S/201295	S/201296	S/201297	S/201298	S/201299
Date Tested :	15/06/2023	15/06/2023	15/06/2023	15/06/2023	15/06/2023	15/06/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	09:40	09:50	10:00	10:10	10:20	10:30
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499116	E 499103	E 499114	E 499102	E 499114	E 499107
Location 2 :	N 6932323	N 6932324	N 6932316	N 6932308	N 6932301	N 6932297
Location 3 :	RL 66.84	RL 66.79	RL 66.74	RL 66.88	RL 66.94	RL 66.87
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	10%	11%	7%	8%	9%	7%
Oversize Density - Dry (t/m ³) :	2.18	2.26	2.18	2.12	2.18	2.16
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/201294	S/201295	S/201296	S/201297	S/201298	S/201299
MDR Test Date :	20/06/2023	20/06/2023	20/06/2023	20/06/2023	20/06/2023	20/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Sandy Gravelly CLAY - Brown	Sandy Gravelly CLAY - Brown	Sandy Gravelly CLAY - Brown	Sandy Gravelly CLAY - Brown	Sandy Gravelly CLAY - Brown	Sandy Gravelly CLAY - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.01	2.04	2.02	2.10	2.14	2.13
Moisture Variation :	2.5%	2.0%	2.5%	2.0%	2.0%	2.0%
ADJ PCWD (t/m ³) :	2.02	2.06	2.03	2.10	2.15	2.14
ADJ Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.0%	2.0%
<i>Moisture Test Results :</i>						
Field Moisture Content :	9.5%	9.5%	10.5%	9.5%	8.5%	9.5%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.03	2.07	2.05	2.12	2.12	2.14
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	100.5%	100.5%	101.0%	100.5%	99.0%	100.0%
Remarks :						
 <p>Accredited for Compliance with ISO/IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast</p> <p>Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  Nick Dobson - Signatory		



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth 99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Number :	SR/PTP/11755 - 33/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	23/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 1 of 2		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/202208	S/202209	S/202210	S/202211	S/202212	S/202213
Date Tested :	21/06/2023	21/06/2023	21/06/2023	21/06/2023	21/06/2023	21/06/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	10:30	10:40	10:50	11:00	11:10	11:20
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499182	E 499198	E 499210	E 499227	E 499241	E 499253
Location 2 :	N 6932279	N 6932280	N 6932267	N 6932270	N 6932256	N 6932262
Location 3 :	RL 60.80	RL 60.76	RL 60.60	RL 60.47	RL 59.30	RL 59.15
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/202208	S/202209	S/202210	S/202211	S/202212	S/202213
MDR Test Date :	23/06/2023	23/06/2023	23/06/2023	23/06/2023	23/06/2023	23/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.14	2.08	2.03	2.10	2.05	2.03
Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.0%	2.5%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	12.5%	12.0%	13.5%	13.0%	14.0%	13.5%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.5% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.12	2.07	2.04	2.11	2.06	2.04
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	99.5%	99.5%	100.5%	100.5%	101.0%	100.5%
Remarks :						
 Accredited for Compliance with ISO/IEC 17025 - Testing Protest Engineering (Darra) Accreditation Number - 2851 Base Laboratory Site Number - 2844 - Darra Base Laboratory Address - 1/35 Limestone Street, Darra, QLD 4076				APPROVED SIGNATORY  Nick Dobson - Signatory		



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/11755 - 33/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	23/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 2 of 2		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/202214	S/202215	S/202216	S/202217	S/202218	S/202219
Date Tested :	21/06/2023	21/06/2023	21/06/2023	21/06/2023	21/06/2023	21/06/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	11:30	11:40	11:50	12:00	12:10	12:20
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499259	E 499239	E 499223	E 499197	E 499185	E 499172
Location 2 :	N 6932254	N 6932271	N 6932261	N 6932271	N 6932270	N 6932280
Location 3 :	RL 59.17	RL 59.10	RL 58.17	RL 59.10	RL 58.07	RL 56.80
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	10%	0%	15%	12%	16%	7%
Oversize Density - Dry (t/m ³) :	2.23	-	2.18	2.28	2.11	2.35
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/202214	S/202215	S/202216	S/202217	S/202218	S/202219
MDR Test Date :	22/06/2023	22/06/2023	22/06/2023	22/06/2023	22/06/2023	22/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.06	2.07	2.06	2.07	2.08	2.06
Moisture Variation :	1.5%	1.5%	1.5%	1.5%	1.5%	1.5%
ADJ PCWD (t/m ³) :	2.08	-	2.08	2.09	2.08	2.07
ADJ Moisture Variation :	1.5%	-	1.0%	1.0%	1.5%	1.5%
<i>Moisture Test Results :</i>						
Field Moisture Content :	12.0%	12.5%	9.5%	10.0%	12.5%	15.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	1.5% Dry of OMC	1.5% Dry of OMC	1.0% Dry of OMC	1.0% Dry of OMC	1.5% Dry of OMC	1.5% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.08	2.03	2.05	2.11	2.06	2.08
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	100.0%	98.0%	98.5%	101.0%	98.5%	100.0%
Remarks :						
 <p>Accredited for Compliance with ISO / IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>		

Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth 99 Sandalwood Lane, Forest Glen, 4556, QLD				Report Number :	SR/PTP/11755 - 34/1
Client Address :	Everleigh Precinct 8 and 10 BEW - LV1				Report Date :	26/06/2023
Project Name :	PTP/11755				Test Request :	-
Project Number :	Lyons				Page 1 of 2	
Location :						
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/202028	S/202029	S/202030	S/202031	S/202032	S/202033
Date Tested :	20/06/2023	20/06/2023	20/06/2023	20/06/2023	20/06/2023	20/06/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	10:10	10:20	10:30	10:40	10:50	11:00
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499058	E 499050	E 499044	E 499038	E 499037	E 499018
Location 2 :	N 6932397	N 6932389	N 6932385	N 6932385	N 6932380	N 6932365
Location 3 :	RL 69.12	RL 69.10	RL 69.17	RL 69.15	RL 69.09	RL 69.21
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/202028	S/202029	S/202030	S/202031	S/202032	S/202033
MDR Test Date :	23/06/2023	23/06/2023	23/06/2023	23/06/2023	23/06/2023	23/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.03	2.07	2.01	2.02	2.03	2.02
Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.0%	2.0%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	10.0%	9.0%	11.0%	12.0%	10.5%	11.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.03	2.05	2.02	2.04	2.03	2.04
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	100.0%	99.0%	100.5%	101.0%	100.0%	100.5%
Remarks :						
 <p>Accredited for Compliance with ISO/IEC 17025 - Testing Protest Engineering (Darra) Accreditation Number - 2851 Base Laboratory Site Number - 2844 - Darra</p> <p>Base Laboratory Address - 1/35 Limestone Street, Darra, QLD 4076</p>				<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>		

Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth 99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Number :	SR/PTP/11755 - 34/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	26/06/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 2 of 2		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/202034	S/202035	S/202036	S/202037	S/202038	S/202039
Date Tested :	20/06/2023	20/06/2023	20/06/2023	20/06/2023	20/06/2023	20/06/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	11:10	11:20	11:30	11:40	11:50	12:00
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499161	E 499170	E 499171	E 499163	E 499156	E 499150
Location 2 :	N 6932326	N 6932329	N 6932324	N 6932337	N 6932335	N 6932334
Location 3 :	RL 63.20	RL 62.80	RL 62.76	RL 63.47	RL 64.04	RL 64.16
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/202034	S/202035	S/202036	S/202037	S/202038	S/202039
MDR Test Date :	23/06/2023	23/06/2023	23/06/2023	23/06/2023	23/06/2023	23/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Clayey SAND - Brown	Gravelly SAND Trace Clay	Clayey SAND - Brown	Clayey SAND - Yellow	Clayey SAND - Brown	Clayey SAND - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.06	2.04	2.09	2.05	2.06	2.08
Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.0%	2.0%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	11.0%	12.0%	9.5%	9.0%	9.5%	9.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.06	2.05	2.08	2.03	2.05	2.06
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	100.0%	100.5%	99.5%	99.0%	99.5%	99.0%
Remarks :						
 <p>Accredited for Compliance with ISO/IEC 17025 - Testing Protest Engineering (Darra) Accreditation Number - 2851 Base Laboratory Site Number - 2844 - Darra</p> <p>Base Laboratory Address - 1/35 Limestone Street, Darra, QLD 4076</p>				<p>APPROVED SIGNATORY</p>  Nick Dobson - Signatory		

Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth	Report Number :	SR/PTP/11755 - 36/1
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD	Report Date :	5/07/2023
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1	Test Request :	-
Project Number :	PTP/11755	Page 1 of 2	
Location :	Lyons		

Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,
----------------	---

Sample Number :	S/202476	S/202477	S/202478	S/202479	S/202480	S/202481
Date Tested :	22/06/2023	22/06/2023	22/06/2023	22/06/2023	22/06/2023	22/06/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175

Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	12:50	13:00	13:10	13:20	13:30	13:40
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499175	E 499189	E 499202	E 499211	E 499228	E 499241
Location 2 :	N 6932305	N 6932306	N 6932304	N 6932293	N 6932297	N 6932293
Location 3 :	RL 60.13	RL 60.06	RL 59.89	RL 59.74	RL 59.70	RL 59.12
Location 4 :	-	-	-	-	-	-



Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/202476	S/202477	S/202478	S/202479	S/202480	S/202481
MDR Test Date :	27/06/2023	27/06/2023	27/06/2023	27/06/2023	27/06/2023	27/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown

<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.05	2.09	2.12	2.11	2.06	2.07
Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.0%	2.0%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-



<i>Moisture Test Results :</i>						
Field Moisture Content :	12.5%	12.5%	12.5%	11.5%	12.5%	12.5%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A

<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.04	2.05	2.04	2.08	2.03	2.06
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	99.0%	98.0%	96.5%	98.5%	98.5%	99.5%



Remarks :	
-----------	--

 <p>Accredited for Compliance with ISO/ IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>	<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>
--	---



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/11755 - 38/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	18/07/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 1 of 2		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/202764	S/202765	S/202766	S/202767	S/202768	S/202769
Date Tested :	23/06/2023	23/06/2023	23/06/2023	23/06/2023	23/06/2023	23/06/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	10:00	10:10	10:20	10:30	10:40	10:50
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499185	E 499186	E 499182	E 499191	E 499198	E 499213
Location 2 :	N 6932335	N 6932332	N 6932325	N 6932330	N 6932327	N 6932331
Location 3 :	RL 61.10	RL 61.12	RL 61.20	RL 61.17	RL 61.04	RL 60.80
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/202764	S/202765	S/202766	S/202767	S/202768	S/202769
MDR Test Date :	28/06/2023	28/06/2023	28/06/2023	28/06/2023	28/06/2023	28/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.05	2.06	2.06	2.06	2.06	2.05
Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.0%	2.0%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	12.5%	12.5%	12.5%	12.5%	12.0%	12.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.06	2.07	2.05	2.08	2.10	2.04
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	100.5%	100.5%	99.5%	101.0%	102.0%	99.5%
Remarks :						
 <p>Accredited for Compliance with ISO/ IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast</p> <p>Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  Nick Dobson - Signatory		

Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/11755 - 38/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	18/07/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 2 of 2		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/202770	S/202771	S/202772	S/202773	S/202774	S/202775
Date Tested :	23/06/2023	23/06/2023	23/06/2023	23/06/2023	23/06/2023	23/06/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	11:00	11:10	11:20	11:30	11:40	11:50
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499217	E 499230	E 499237	E 499252	E 499255	E 499270
Location 2 :	N 6932321	N 6932329	N 6932318	N 6932324	N 6932312	N 6932320
Location 3 :	RL 60.74	RL 60.43	RL 59.89	RL 59.90	RL 59.88	RL 59.60
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/202770	S/202771	S/202772	S/202773	S/202774	S/202775
MDR Test Date :	28/06/2023	28/06/2023	28/06/2023	28/06/2023	28/06/2023	28/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Sandy CLAY trace Gravel - Brown	Sandy CLAY trace Gravel - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY trace Gravel - Brown	Sandy CLAY trace Gravel - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.07	2.07	2.07	2.03	2.06	2.06
Moisture Variation :	2.0%	2.0%	2.0%	2.0%	1.5%	2.0%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	12.5%	12.0%	10.5%	11.0%	13.0%	11.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	1.5% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.07	2.05	2.07	2.09	2.06	2.06
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	99.5%	99.0%	100.5%	103.0%	100.0%	100.0%
Remarks :						
 Accredited for Compliance with ISO/IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208				APPROVED SIGNATORY  Nick Dobson - Signatory		

Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/11755 - 39/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	18/07/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 1 of 2		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/203123	S/203124	S/203125	S/203126	S/203127	S/203128
Date Tested :	26/06/2023	26/06/2023	26/06/2023	26/06/2023	26/06/2023	26/06/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	11:30	11:40	11:50	12:00	12:10	12:20
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499164	E 499171	E 499179	E 499189	E 499190	E 499200
Location 2 :	N 6932323	N 6932318	N 6932316	N 6932326	N 6932318	N 6932318
Location 3 :	RL 61.90	RL 61.88	RL 61.79	RL 60.89	RL 60.94	RL 60.66
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Override Wet :	0%	0%	0%	0%	0%	0%
Override Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/203123	S/203124	S/203125	S/203126	S/203127	S/203128
MDR Test Date :	29/06/2023	29/06/2023	29/06/2023	29/06/2023	29/06/2023	29/06/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.03	2.06	2.07	2.03	2.11	2.03
Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.0%	2.0%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	10.5%	10.0%	11.0%	10.5%	11.0%	10.5%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.05	2.07	2.03	2.05	2.04	2.09
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	101.0%	100.5%	98.5%	101.5%	97.0%	102.5%
Remarks :						
 <p>Accredited for Compliance with ISO/ IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>		

Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth	Report Number :	SR/PTP/11755 - 43/1
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD	Report Date :	18/07/2023
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1	Test Request :	-
Project Number :	PTP/11755	Page 1 of 2	
Location :	Lyons		

Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,
----------------	---

Sample Number :	S/204156	S/204157	S/204158	S/204159	S/204160	S/204161
Date Tested :	30/06/2023	30/06/2023	30/06/2023	30/06/2023	30/06/2023	30/06/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175

Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	11:40	11:50	12:00	12:10	12:20	12:30
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499383	E 499389	E 499387	E 499382	E 499402	E 499380
Location 2 :	N 6932311	N 6932314	N 6932309	N 6932307	N 6932304	N 6932304
Location 3 :	RL 57.80	RL 57.84	RL 57.69	RL 58.04	RL 58.12	RL 58.21
Location 4 :	-	-	-	-	-	-



Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Over size Wet :	0%	0%	4%	0%	11%	5%
Over size Density - Dry (t/m ³) :	-	-	2.02	-	2.10	2.12
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/204156	S/204157	S/204158	S/204159	S/204160	S/204161
MDR Test Date :	6/07/2023	6/07/2023	6/07/2023	6/07/2023	6/07/2023	6/07/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown

<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.06	2.06	2.05	2.05	2.07	2.06
Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.0%	2.0%
ADJ PCWD (t/m ³) :	-	-	2.05	-	2.08	2.06
ADJ Moisture Variation :	-	-	2.0%	-	2.0%	2.0%



<i>Moisture Test Results :</i>						
Field Moisture Content :	8.0%	8.0%	7.5%	8.0%	8.5%	7.5%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A

<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.03	2.05	2.03	2.05	2.04	2.02
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	98.5%	99.0%	99.0%	100.0%	98.5%	98.0%

Remarks :	
-----------	--

 <p>Accredited for Compliance with ISO/ IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>	<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>
--	---

Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/11755 - 47/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	25/07/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 1 of 1		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/205914	S/205918	S/205919	S/205920	S/205921	S/205922
Date Tested :	11/07/2023	11/07/2023	11/07/2023	11/07/2023	11/07/2023	11/07/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	10:30	10:45	11:00	11:15	11:30	11:45
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499265	E 499295	E 499310	E 499349	E 499387	E 499414
Location 2 :	N 6932285	N 6932297	N 6932280	N 6932281	N 6932267	N 6932283
Location 3 :	RL 5.22	RL 5.22	RL 5.22	RL 5.22	RL 5.22	RL 5.22
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	0%	0%	0%	0%	0%	0%
Oversize Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/205914	S/205918	S/205919	S/205920	S/205921	S/205922
MDR Test Date :	19/07/2023	19/07/2023	19/07/2023	19/07/2023	19/07/2023	19/07/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Gravelly Sandy CLAY - Light Brown	Gravelly Sandy CLAY - Light Brown	Gravelly Sandy CLAY - Light Brown	Gravelly Sandy CLAY - Light Brown	Gravelly Sandy CLAY - Light Brown	Gravelly Sandy CLAY - Light Brown
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.11	2.15	2.12	2.10	2.11	2.12
Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.0%	2.0%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-
<i>Moisture Test Results :</i>						
Field Moisture Content :	9.5%	9.0%	9.0%	9.5%	9.5%	9.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.13	2.15	2.13	2.12	2.13	2.13
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	100.5%	100.0%	100.0%	101.0%	101.0%	100.5%
Remarks :						
 <p>Accredited for Compliance with ISO/ IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>		

Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth	Report Number :	SR/PTP/11755 - 48/1
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD	Report Date :	25/07/2023
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1	Test Request :	-
Project Number :	PTP/11755	Page 1 of 1	
Location :	Lyons		

Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,
----------------	---

Sample Number :	S/206199	S/206200	S/206201	S/206202	S/206203	S/206204
Date Tested :	12/07/2023	12/07/2023	12/07/2023	12/07/2023	12/07/2023	12/07/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175

Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	12:30	12:40	12:50	13:00	13:10	13:20
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499105	E 499107	E 499110	E 499070	E 499072	E 499112
Location 2 :	N 6932415	N 6932409	N 6932413	N 6932322	N 6932309	N 6932319
Location 3 :	Finish Level	Finish Level	Finish Level	Finish Level	Finish Level	Finish Level
Location 4 :	-	-	-	-	-	-



Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Override Wet :	0%	0%	0%	0%	0%	0%
Override Density - Dry (t/m ³) :	-	-	-	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/206199	S/206200	S/206201	S/206202	S/206203	S/206204
MDR Test Date :	20/07/2023	20/07/2023	20/07/2023	20/07/2023	20/07/2023	20/07/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown

<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.06	2.06	2.01	2.09	2.05	2.02
Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.0%	2.0%
ADJ PCWD (t/m ³) :	-	-	-	-	-	-
ADJ Moisture Variation :	-	-	-	-	-	-



<i>Moisture Test Results :</i>						
Field Moisture Content :	9.5%	10.5%	11.0%	9.0%	10.5%	11.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A

<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.06	2.07	2.03	2.06	2.06	2.04
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	99.5%	100.5%	101.5%	99.0%	100.5%	101.0%



Remarks :	
-----------	--

 <p>Accredited for Compliance with ISO/ IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>	<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>
--	---

Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/11755 - 49/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	25/07/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 1 of 2		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/206397	S/206402	S/206403	S/206404	S/206405	S/206406
Date Tested :	13/07/2023	13/07/2023	13/07/2023	13/07/2023	13/07/2023	13/07/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	12:50	13:00	13:10	13:20	13:30	13:40
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499026	E 499034	E 499021	E 499028	E 499016	E 499010
Location 2 :	N 6932406	N 6932411	N 6932403	N 6932413	N 6932400	N 6932402
Location 3 :	RL 69.21	RL 69.26	RL 69.18	RL 69.20	RL 69.40	RL 69.37
Location 4 :	-	-	-	-	-	-
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Oversize Wet :	11%	14%	8%	16%	10%	11%
Oversize Density - Dry (t/m ³) :	2.07	2.13	2.08	2.21	2.05	2.04
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/206397	S/206402	S/206403	S/206404	S/206405	S/206406
MDR Test Date :	21/07/2023	21/07/2023	21/07/2023	21/07/2023	21/07/2023	21/07/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Brown	Clayey SAND - Yellow	Clayey SAND - Yellow
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.10	2.09	2.10	2.10	2.09	2.06
Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.0%	2.0%
ADJ PCWD (t/m ³) :	2.10	2.10	2.10	2.11	2.08	2.06
ADJ Moisture Variation :	2.0%	2.0%	2.0%	2.0%	2.0%	2.0%
<i>Moisture Test Results :</i>						
Field Moisture Content :	9.5%	9.5%	10.5%	9.0%	10.5%	10.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.10	2.08	2.11	2.09	2.10	2.07
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	100.0%	99.0%	100.5%	99.0%	100.5%	100.5%
Remarks :						
 <p>Accredited for Compliance with ISO/ IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>		

Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth		Report Number :	SR/PTP/11755 - 49/1		
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD		Report Date :	25/07/2023		
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1		Test Request :	-		
Project Number :	PTP/11755		Page 2 of 2			
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/206407	S/206408				
Date Tested :	13/07/2023	13/07/2023				
Material Source :	Onsite	Onsite				
For use as :	General Fill	General Fill				
Test / Layer Depths :	150 / 175	150 / 175				
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b				
Time :	13:50	14:00				
Lot Number :	-	-				
Location 1 :	E 499040	E 499047				
Location 2 :	N 6932418	N 6932428				
Location 3 :	RL 69.43	RL 69.45				
Location 4 :	-	-				
Test Fraction (mm) :	< 19mm	< 19mm				
Oversize Wet :	14%	13%				
Oversize Density - Dry (t/m ³) :	1.99	2.07				
Assigned MDR (Yes/No) :	No	No				
MDR Sample Number :	S/206407	S/206408				
MDR Test Date :	21/07/2023	21/07/2023				
Compaction Type :	Standard	Standard				
Soil Description :	Clayey SAND - Yellow	Clayey SAND - Yellow				
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.10	2.03				
Moisture Variation :	2.0%	2.5%				
ADJ PCWD (t/m ³) :	2.09	2.04				
ADJ Moisture Variation :	2.0%	2.0%				
<i>Moisture Test Results :</i>						
Field Moisture Content :	9.5%	10.0%				
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC				
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC				
Relative Moisture Ratio (Q250) :	-	-				
Moisture Ratio :	N/A	N/A				
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.11	2.08				
Density Specification :	95%	95%				
Wet Density Ratio :	101.5%	102.0%				
Remarks :						
 <p>Accredited for Compliance with ISO/ IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>			<p>APPROVED SIGNATORY</p>  Nick Dobson - Signatory			

Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth	Report Number :	SR/PTP/11755 - 51/1
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD	Report Date :	7/08/2023
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1	Test Request :	-
Project Number :	PTP/11755	Page 1 of 1	
Location :	Lyons		

Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,
----------------	---

Sample Number :	S/207405	S/207406	S/207407	S/207408	S/207409	S/207410
Date Tested :	19/07/2023	19/07/2023	19/07/2023	19/07/2023	19/07/2023	19/07/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175	150 / 175

Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	12:30	12:40	12:50	13:00	13:10	13:30
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499014	E 499021	E 499031	E 499036	E 499049	E 499005
Location 2 :	N 6932412	N 6932421	N 6932422	N 6932435	N 6932419	N 6932395
Location 3 :	RL 69.50	RL 69.57	RL 69.37	RL 69.44	RL 69.60	RL 69.63
Location 4 :	-	-	-	-	-	-



Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm	< 19mm
Override Wet :	0%	0%	5%	0%	0%	0%
Override Density - Dry (t/m ³) :	-	-	1.86	-	-	-
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/207405	S/207406	S/207407	S/207408	S/207409	S/207410
MDR Test Date :	27/07/2023	27/07/2023	27/07/2023	27/07/2023	27/07/2023	27/07/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown

<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.04	2.07	2.04	2.06	2.02	2.06
Moisture Variation :	2.0%	2.0%	2.0%	1.5%	1.5%	2.0%
ADJ PCWD (t/m ³) :	-	-	2.03	-	-	-
ADJ Moisture Variation :	-	-	2.0%	-	-	-

<i>Moisture Test Results :</i>						
Field Moisture Content :	10.0%	9.5%	8.5%	9.0%	10.5%	10.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	1.5% Dry of OMC	1.5% Dry of OMC	2.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A

<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.06	2.09	2.06	2.09	2.07	2.07
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	100.5%	101.0%	101.5%	101.0%	102.0%	101.0%

Remarks :	
-----------	--

 <p>Accredited for Compliance with ISO/ IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>	<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>
--	---

Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth	Report Number :	SR/PTP/11755 - 58/1
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD	Report Date :	14/08/2023
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1	Test Request :	-
Project Number :	PTP/11755	Page 1 of 2	
Location :	Lyons		

Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,
----------------	---

Sample Number :	S/209321	S/209322	S/209323	S/209324	S/209325	S/209326
Date Tested :	27/07/2023	27/07/2023	27/07/2023	27/07/2023	27/07/2023	27/07/2023
Material Source :	Onsite	Onsite	Onsite	Onsite	Onsite	Onsite
For use as :	General Fill	General Fill	General Fill	General Fill	General Fill	General Fill
Test / Layer Depths :	175 / 200	175 / 200	175 / 200	175 / 200	175 / 200	175 / 200

Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b
Time :	11:00	11:10	11:20	11:30	11:40	11:50
Lot Number :	-	-	-	-	-	-
Location 1 :	E 499056	E 499033	E 499074	E 499101	E 499129	E 499143
Location 2 :	N 6932494	N 6932525	N 6932509	N 6932503	N 6932391	N 6932382
Location 3 :	0.9m Below Finish Level	1.2m Below Finish Level	1.5m Below Finish Level	0.9m Below Finish Level	Finish Level	0.6m Below Finish Level
Location 4 :	-	-	-	-	-	-



Test Fraction (mm) :	< 37.5mm	< 37.5mm	< 37.5mm	< 37.5mm	< 37.5mm	< 37.5mm
Oversize Wet :	11%	7%	18%	7%	13%	14%
Oversize Density - Dry (t/m ³) :	2.20	2.17	2.20	2.19	2.17	2.15
Assigned MDR (Yes/No) :	No	No	No	No	No	No
MDR Sample Number :	S/209321	S/209322	S/209323	S/209324	S/209325	S/209326
MDR Test Date :	9/08/2023	9/08/2023	9/08/2023	9/08/2023	9/08/2023	9/08/2023
Compaction Type :	Standard	Standard	Standard	Standard	Standard	Standard
Soil Description :	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown	Gravelly Clayey SAND - Brown

<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.22	2.23	2.23	2.23	2.23	2.24
Moisture Variation :	2.0%	2.5%	2.0%	2.0%	1.0%	1.0%
ADJ PCWD (t/m ³) :	2.22	2.22	2.23	2.23	2.23	2.22
ADJ Moisture Variation :	2.0%	2.0%	1.5%	2.0%	1.0%	1.0%



<i>Moisture Test Results :</i>						
Field Moisture Content :	6.0%	6.5%	5.5%	7.0%	5.0%	5.0%
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	1.5% Dry of OMC	2.0% Dry of OMC	1.0% Dry of OMC	1.0% Dry of OMC
Relative Moisture Ratio (Q250) :	-	-	-	-	-	-
Moisture Ratio :	N/A	N/A	N/A	N/A	N/A	N/A

<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.23	2.21	2.20	2.21	2.22	2.20
Density Specification :	95%	95%	95%	95%	95%	95%
Wet Density Ratio :	100.5%	99.5%	99.0%	99.0%	99.5%	99.0%



Remarks :	
-----------	--

 <p>Accredited for Compliance with ISO/ IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>	<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>
--	---



Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/11755 - 58/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	14/08/2023	
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1			Test Request :	-	
Project Number :	PTP/11755			Page 2 of 2		
Location :	Lyons					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/209327	S/209328	S/209329			
Date Tested :	27/07/2023	27/07/2023	27/07/2023			
Material Source :	Onsite	Onsite	Onsite			
For use as :	General Fill	General Fill	General Fill			
Test / Layer Depths :	175 / 200	175 / 200	175 / 200			
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b			
Time :	12:00	12:10	12:20			
Lot Number :	-	-	-			
Location 1 :	E 499148	E 499159	E 499166			
Location 2 :	N 6932369	N 6932363	N 6932352			
Location 3 :	0.3m Below Finish Level	0.3m Below Finish Level	Finish Level			
Location 4 :	-	-	-			
Test Fraction (mm) :	< 37.5mm	< 37.5mm	< 37.5mm			
Oversize Wet :	12%	10%	13%			
Oversize Density - Dry (t/m ³) :	2.16	2.21	2.23			
Assigned MDR (Yes/No) :	No	No	No			
MDR Sample Number :	S/209327	S/209328	S/209329			
MDR Test Date :	10/08/2023	10/08/2023	10/08/2023			
Compaction Type :	Standard	Standard	Standard			
Soil Description :	Gravelly SAND Brown	Gravelly SAND Brown	Gravelly SAND Brown			
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.29	2.29	2.30			
Moisture Variation :	2.0%	2.0%	1.5%			
ADJ PCWD (t/m ³) :	2.27	2.28	2.29			
ADJ Moisture Variation :	1.5%	1.5%	1.5%			
<i>Moisture Test Results :</i>						
Field Moisture Content :	5.5%	6.0%	5.5%			
Moisture Specification :	+/-2.0% of OMC	+/-2.0% of OMC	+/-2.0% of OMC			
Variation from OMC :	1.5% Dry of OMC	1.5% Dry of OMC	1.5% Dry of OMC			
Relative Moisture Ratio (Q250) :	-	-	-			
Moisture Ratio :	N/A	N/A	N/A			
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.22	2.20	2.21			
Density Specification :	95%	95%	95%			
Wet Density Ratio :	98.0%	96.5%	96.5%			
Remarks :						
 <p>Accredited for Compliance with ISO/ IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>				<p>APPROVED SIGNATORY</p>  Nick Dobson - Signatory		

Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth			Report Number :	SR/PTP/10047 - 106/1	
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD			Report Date :	20/04/2023	
Project Name :	Everleigh Estate - Precinct 9.4 Earthworks			Test Request :	-	
Project Number :	PTP/10047			Page 1 of 1		
Location :	Greenbank					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/190919	S/190920	S/190921			
Date Tested :	12/04/2023	12/04/2023	12/04/2023			
Material Source :	Onsite	Onsite	Onsite			
For use as :	General Fill	General Fill	General Fill			
Test / Layer Depths :	175 / 150	175 / 150	175 / 150			
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b			
Time :	11:50	11:51	11:51			
Lot Number :	-	-	-			
Location 1 :	E 499382	E 499364	E 499344			
Location 2 :	N 6932161	N 6932164	N 6932200			
Location 3 :	0.6m Below Finish Level	0.6m Below Finish Level	0.6m Below Finish Level			
Location 4 :	-	-	-			
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm			
Oversize Wet :	18%	17%	17%			
Oversize Density - Dry (t/m ³) :	2.21	2.10	2.27			
Assigned MDR (Yes/No) :	No	No	No			
MDR Sample Number :	S/190919	S/190920	S/190921			
MDR Test Date :	19/04/2023	19/04/2023	19/04/2023			
Compaction Type :	Standard	Standard	Standard			
Soil Description :	Gravelly Clayey Sand - Brown	Gravelly Clayey Sand - Brown	Gravelly Clayey Sand - Brown			
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.11	2.11	2.15			
Moisture Variation :	3.0%	2.5%	2.0%			
ADJ PCWD (t/m ³) :	2.13	2.11	2.17			
ADJ Moisture Variation :	2.5%	2.5%	2.0%			
<i>Moisture Test Results :</i>						
Field Moisture Content :	7.0%	7.5%	7.0%			
Moisture Specification :	-	-	-			
Variation from OMC :	2.5% Dry of OMC	2.5% Dry of OMC	2.0% Dry of OMC			
Relative Moisture Ratio (Q250) :	-	-	-			
Moisture Ratio :	N/A	N/A	N/A			
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.16	2.16	2.22			
Density Specification :	95%	95%	95%			
Wet Density Ratio :	101.5%	102.5%	102.5%			
Remarks :						
 <p>Accredited for Compliance with ISO/ IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>	APPROVED SIGNATORY  Ben Pittard - Signatory					

Soil Compaction and Density Tests Report - Compaction Control

Client :	Shadforth 99 Sandalwood Lane, Forest Glen, 4556, QLD				Report Number :	SR/PTP/10047 - 118/1
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD				Report Date :	24/05/2023
Project Name :	Everleigh Estate - Precinct 9.4 Earthworks				Test Request :	-
Project Number :	PTP/10047				Page 1 of 1	
Location :	Greenbank					
Test Methods :	AS1289.5.4.1, AS1289.5.8.1, AS1289.2.1.1, AS1289.5.7.1,					
Sample Number :	S/189946	S/189950	S/189951	S/189952		
Date Tested :	5/04/2023	5/04/2023	5/04/2023	5/04/2023		
Material Source :	Onsite	Onsite	Onsite	Onsite		
For use as :	General Fill	General Fill	General Fill	General Fill		
Test / Layer Depths :	150 / 175	150 / 175	150 / 175	150 / 175		
Sampling Method :	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b	AS1289.1.2.1 - cl6.4b		
Time :	08:30	08:45	09:00	09:15		
Lot Number :	-	-	-	-		
Location 1 :	E 499331	E 499381	E 499428	E 499490		
Location 2 :	N 6932172	N 6932155	N 6932135	N 6932093		
Location 3 :	0.6m Below Finish Level	0.6m Below Finish Level	0.6m Below Finish Level	0.6m Below Finish Level		
Location 4 :	-	-	-	-		
Test Fraction (mm) :	< 19mm	< 19mm	< 19mm	< 19mm		
Oversize Wet :	12%	18%	0%	18%		
Oversize Density - Dry (t/m ³) :	2.24	2.03	-	2.16		
Assigned MDR (Yes/No) :	No	No	No	No		
MDR Sample Number :	S/189946	S/189950	S/189951	S/189952		
MDR Test Date :	13/04/2023	13/04/2023	13/04/2023	13/04/2023		
Compaction Type :	Standard	Standard	Standard	Standard		
Soil Description :	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown	Sandy CLAY - Brown		
<i>MDR Test Results</i>						
PCWD (t/m ³) :	2.15	2.20	2.18	2.15		
Moisture Variation :	2.0%	2.0%	2.0%	2.0%		
ADJ PCWD (t/m ³) :	2.16	2.17	-	2.15		
ADJ Moisture Variation :	2.0%	2.0%	-	1.5%		
<i>Moisture Test Results</i>						
Field Moisture Content :	8.0%	8.0%	10.0%	8.5%		
Moisture Specification :	±2% of OMC	±2% of OMC	±2% of OMC	±2% of OMC		
Variation from OMC :	2.0% Dry of OMC	2.0% Dry of OMC	2.0% Dry of OMC	1.5% Dry of OMC		
Relative Moisture Ratio (Q250) :	-	-	-	-		
Moisture Ratio :	N/A	N/A	N/A	N/A		
<i>Density Test Results</i>						
Field Wet Density (t/m ³) :	2.21	2.20	2.20	2.19		
Density Specification :	95%	95%	95%	95%		
Wet Density Ratio :	102.0%	101.5%	101.0%	101.5%		
Remarks :						
 <p>Accredited for Compliance with ISO/IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>	<p>APPROVED SIGNATORY</p>  <p>Nick Dobson - Signatory</p>					
	Document Number : RF1	Date : 12/03/2023				

Particle Size Distribution Report

Client :	Shadforths	Report Number :	SR/PTP/11755 - 82/1
Client Address :	99 Sandalwood Lane, Forest Glen, 4556, QLD	Report Date :	24/01/2024
Project Name :	Everleigh Precinct 8 and 10 BEW - LV1	Test Request :	-
Project Number :	PTP/11755	Page 1 of 1	
Location :	Lyons		

Test Methods :	Q103A, AS1289.2.1.1,
----------------	----------------------

Material Description	(GW) Clayey Sandy GRAVEL, Well Graded, Brown, Moist
----------------------	---

Sample Number :	S/236920	Sampling Method :	AS1289.1.2.1 - cl6.4b
Date Tested :	19/01/2024	Time :	12:15
Material Source :	Onsite	Location 1 :	Precinct 10.2 - Top 600
For Use As :	General Fill (Lot)	Location 2 :	E 499135
Lot Number :	-	Location 3 :	N 6932377
PSD Specification Number :	N/A	Location 4 :	Finish Level

AS Sieve Size (mm) :	Percent Passing (%) :	Specification Limits :	
75.0	83		<div style="text-align: center;"> <p>Particle Size Distribution Graph</p> </div>
63.0			
53.0	72		
37.5	66		
26.5	63		
19.0	58		
16			
13.2			
9.5	53		
6.7			
4.75	49		
2.36	47		
1.18			
0.600			
0.425	36		
0.300			
0.150			
0.075	13		

Remarks :	-
-----------	---

<p style="margin: 0;">Accredited for Compliance with ISO/ IEC 17025 - Testing Protest Engineering (Gold Coast) Accreditation Number - 19667 Base Laboratory Site Number - 22838 - Gold Coast Base Laboratory Address - 8/36 Blanck Street, ORMEAU, QLD 4208</p>	<p style="margin: 0;">APPROVED SIGNATORY</p> <p style="margin: 0;">Joshua Andres - Signatory</p>
--	---
